

Meeting Minutes
Farmington High School Building Committee Meeting
FHS Library/ZOOM Webinar
Wednesday, September 20, 2023
5:00 P.M.

Attendees:

Meg Guerrera, Chair
Johnny Carrier
Sarah Healey
Suraj Kurtakoti
Michael Smith (via ZOOM)
Chris Fagan (via ZOOM)
Wendy Ku (via ZOOM)
Beth Kintner
Kathy Greider, Superintendent of Schools
Scott Hurwitz, Asst. Superintendent of Finance & Operations
Sam Kilpatrick, Director of School Facilities
Kat Krajewski, Assistant Town Manager
Devon Aldave, Clerk of the Committee
Mark Garilli, Construction Solutions Group
Samantha D'Agostino, Construction Solutions Group
Michael Small, Construction Solutions Group
Ryszard Szczypek, TSKP Studio
Michael Scott, TSKP Studio (via ZOOM)
Nelson Reis, O&G Industries
Michael Kensah, O&G Industries
Mark Jeffko, O&G Industries

A. Call to Order.

The meeting was called to order at 5:04 P.M.

B. Pledge of Allegiance.

The committee members recited the Pledge of Allegiance.

C. Public Comment.

None.

D. Minutes.

1) To approve the attached August 16, 2023, minutes.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the August 16, 2023, minutes.

2) To approve the attached August 30, 2023, minutes.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the August 30, 2023, minutes.

3) To approve the attached September 13, 2023, minutes.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the September 13, 2023, minutes.

E. Correspondence Received 8/15/2023-9/18/2023.

None.

F. Reports.

1) Chair Report.

No report.

2) Town Council Liaison Report.

Johnny Carrier reported that the next Town Council meeting will be held on October 10, 2023.

3) Board of Education Liaison Report.

Beth Kintner reported that Board of Education members toured the FHS construction site earlier today and were impressed with the progress.

4) 1928 Building Committee Liaison Report.

Chris Fagan reported that the Project Architect is holding end user meetings with Town Department Heads in the near future. Silver Petrucelli has met with the FHS Building Committee design team.

5) Owner's Representative Report.

Mark Garilli reported that CSG continues to hold weekly meetings with the professional partners. CSG is working with the State regarding reimbursement.

6) Architect Report.

Ryszard Szczypek reported that he is pleased with the construction progress that has been made. Ryszard stated that the design team has met with the design team for the 1928 Building Project to clarify utility structures and modifications.

Ryszard also reported that the Board of Education unanimously voted to approve plans and project manuals for technology equipment bids. This item is also included on the FHS Building Committee's agenda.

7) Construction Manager Report.

Nelson Reis provided a Construction Manager monthly report which is recorded with these minutes as Attachment A.

8) Communications Subcommittee Report.

No report.

9) Professional Partnership Subcommittee Report.

Kat Krajewski reported that the Professional Partnership Subcommittee will meet in the future to discuss Move Management Services.

10) Financial Subcommittee Report.

Meg Guerrera reported that the Financial Subcommittee met on September 15th and reviewed and approved the invoice packages and other agenda items included on this agenda.

11) Financial Report.

No report.

G. New Business.

1) To approve the following invoice package for Farmington Central Offices:

Name	Amount	Description
Construction Solutions Group	\$1,030.00	Professional Services Central Office (August 2023)

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the invoice package for Farmington Central Offices.

2) To approve the following invoice package for Farmington High School:

Name	Amount	Description
Construction Solutions Group	\$22,597.00	Professional Services (August 2023)
TSKP Studio	\$42,000.00	Professional Service (August 2023)
O&G Industries	\$6,477,393.88	Application #14
IMTL	\$1,100.00	Invoice #5786-F: Materials Testing
IMTL	\$13,838.78	Invoice #5706-I: Materials Testing
Innovative Engineering Services	\$6,908.00	Invoice #18195: Commissioning Services
O&G Industries	\$6,903.00	PCO#32, RFI#222 – AV Systems –

		Addition of 2 UPS Units with 2 Additional 120V Circuits
O&G Industries	\$7,032.00	PCO #33 – End curtains with logo
O&G Industries	\$6,107.00	PCO#34 – Media center telescoping seating custom color carpet
O&G Industries	\$1,336.00	PCO#40 – Ceiling mounted urinal screens
O&G Industries	\$1,076.00	PCO#41, RFI#192 – AED Cabinet – Misc. Equipment Defibrillator
O&G Industries	\$56,882.00	PCO#39, PR#22 – Changes to White Boards and Data Drops
O&G Industries	\$8,615.00	PCO#49 – Communications Racks, Frames, & Enclosures
O&G Industries	\$1,855.00	PCO#51, PR#25 – RFI#266 – AV SR Devices Added & Relocated in Small Group Rooms in Area A and Area B
O&G Industries	(\$20,662.00)	PCO#54, PR#33 – Main Office Room #1321 – Millwork Desk Removal in Area C

Mark Garilli and Nelson Reis reviewed the invoice package with the FHS Building Committee. The amount for O&G's Application #14 was listed incorrectly in the agenda invoice package, but the backup documentation had the correct amount of \$6,477,393.88. The committee amended the package to the correct amount of Application #14.

Mark Garilli and Ryszard Szczypek reviewed PCO#39 with the committee.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the invoice package for Farmington High School as amended.

3) To approve the attached fee proposal from TSKP Studio for FF&E items in the amount of \$18,720.00.

Ryszard Szczypek clarified that the fee proposal from TSKP Studio and Kohler Ronan is for design services for mechanical, electrical, and plumbing changes that are a result of the FF&E process, not for actual FF&E items.

As a result, the FHS Building Committee amended the motion to read the following: To approve the fee proposal from TSKP Studio and Kohler Ronan in the amount of \$18,720.00.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the fee proposal from TSKP Studio and Kohler Ronan in the amount of \$18,720.00.

4) To approve a \$20,000.00 increase to IMTL's purchase order for materials testing.

Mark Garilli and Nelson Reis explained that more materials testing will be needed and the funds in IMTL's existing purchase have been utilized. The professional partners are estimating that roughly \$20,000 more will be needed for these services.

The FHS Building Committee discussed this and determined that these funds should be drawn from contingency.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve a \$20,000 increase to IMTL's purchase order for materials testing.

5) The Farmington High School Building Committee hereby certifies that these final plans and the project manuals as prepared for bidding and dated September 14, 2023, and the professional cost estimate, completed in accordance with Level 3 of ASTM International Standard E1557, Standard Classification of Building Elements and Related Sitework- UNIFORMAT II for the following projects; State Project No. 052-0076N – Farmington High School Technology Equipment Bid Package (Phase 4 of 4) and State Project No. 052-0077BOE – FPS Central Office Technology Equipment Bid Package (Phase 3 of 3) and dated September 14, 2023, have

been reviewed and approved for this project on September 20, 2023.

Matt Ross, Director of Technology for Farmington Public Schools, gave a presentation that summarized the inclusions in the Technology Equipment Bid Packages. This presentation is recorded with these minutes as Attachment B.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously CERTIFIED: that these final plans and the project manuals as prepared for bidding and dated September 14, 2023, and the professional cost estimate, completed in accordance with Level 3 of ASTM International Standard E1557, Standard Classification of Building Elements and Related Sitework-UNIFORMAT II for the following projects; State Project No. 052-0076N – Farmington High School Technology Equipment Bid Package (Phase 4 of 4) and State Project No. 052-0077BOE – FPS Central Office Technology Equipment Bid Package (Phase 3 of 3) and dated September 14, 2023, have been reviewed and approved for this project on September 20, 2023.

6) To approve the attached invoice from Tall Timbers Marketing in the amount of \$7,500.00.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to approve the invoice from Tall Timbers Marketing in the amount of \$7,500.00.

7) To increase the Decision-Making Group's threshold to \$50,000.00.

Kat Krajewski and Johnny Carrier explained that the Decision-Making Group's threshold is currently \$25,000.00. At this point in construction, changes may need to be made quickly. Increasing this group's threshold will allow the project to progress without delays.

8) To cancel the October 4, 2023, FHS Building Committee meeting.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to cancel the October 4, 2023, FHS Building Committee meeting.

H. Executive Session.

1) Discussion regarding a pending claim pertaining to the Farmington High School project in accordance with Section 1-200(6)(B) of the Connecticut General Statutes.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to move to executive session at 6:25 P.M.

Open session resumed at 6:59 P.M.

I. Other Business.

1) To authorize the Town Manager to modify and/or manage the contractual relationship with the Owner's Representative.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to authorize the Town Manager to modify and/or manage the contractual relationship with the Owner's Representative.

J. Adjournment.

Upon a motion made and seconded (Carrier/Kurtakoti) it was unanimously VOTED: to adjourn at 7:02 P.M.

Respectfully Submitted,

Devon Aldave
Clerk of the Committee



September 14 , 2023

Ms. Kathleen Blonski
Town Manager
Town of Farmington
1 Montieth Drive
Farmington, CT 06032

REFERENCE: Farmington High School
O&G Project No. 2013902
Monthly Progress Report No.7

Dear Ms. Blonski,

Enclosed for your information and records is Monthly Progress Report No. 7 through August 2023.

If you have any questions concerning this report, please contact me at your convenience.

Sincerely,
O & G INDUSTRIES, INC.

A handwritten signature in black ink, appearing to read 'Nelson Reis'.

Nelson Reis
Project Manager

NR/LCR
Enclosures
CC: File 2013902
Field

FARMINGTON HIGH SCHOOL

TABLE OF CONTENTS

O & G Staff.....	1
Summary Data.....	2
Construction Manager’s Monthly Cost Control Report	3-6
Owner Changes Log.....	7-16
CM In-Scope Changes Log	17
PCO’s Under Review	18
Cost/Schedule Impact Items	19
Project Commentary.....	20
Project Schedule (Run Date 9/14/23).....	21-84
Project Photos	85-92

MONTHLY PROGRESS REPORT

AUGUST 2023

PROJECT: Farmington High School O&G PROJECT NO.: 2013902

LOCATION: Farmington, Connecticut

OWNER: Town of Farmington O&G STAFF

Project Manager Nelson Reis

Project SuperintendentGeorge Givens

Project Executive Mark Jeffko

Contract Administrator Lynn Robotham

Safety Engineer/Coordinator Jay Emanuel

MEP Coordinator.....Joseph Fucci

Project Engineer.....Mason Coudriet

Assistant Project Manager.....Michael Kensah

Assistant Superintendent.....Evan Nelson

SUMMARY DATA		
August 2023 PROJECT: Farmington High School		Report #7
COMPLETION DATES	ORIGINAL	CURRENT
New High School	7/30/2024	7/30/2024
Building Abatement	10/16/2024	10/16/2024
Central Office Renovations	2/14/2025	2/14/2025
Sitework & Landscaping	5/1/2025	5/1/2025
Commissioning	10/22/2024	10/22/2024
PHYSICAL PROGRESS PERCENTAGE COMPLETE	LAST REPORT	THIS REPORT
New High School	36%	48%
Sitework & Landscaping	33%	41%
Commissioning	5%	5%
Construction Budget	LAST REPORT	THIS REPORT
Baseline Budget	\$124,836,478.00	\$124,836,478.00
GMP Allowances		
Potential Budget Revisions	\$65,356.00	\$3,535.00
Approved Budget Revisions	-\$23,784.00	\$234,134.00
Current Budget (GMP)	\$124,878,050.00	\$125,074,147.00
Construction Costs	LAST REPORT	THIS REPORT
Awarded Contracts	\$119,728,100.00	\$119,728,100.00
Potential Contract Changes	\$158,167.00	\$56,615.00
Approved Contract Changes	-\$43,145.00	\$254,504.00
Projected Costs	\$119,843,122.00	\$120,039,219.00
Pending Contracts		
Projected Costs with Pending Contracts	\$119,843,122.00	\$120,039,219.00
Funds Available	LAST REPORT	THIS REPORT
Allowances		
Funds Available	\$5,034,928.00	\$5,034,929.00
Total Funds Available	\$5,034,928.00	\$5,034,929.00

CM Monthly Cost Control Report

Grouped by WBS. Summarized by Line Item Name.
Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Line Item Name	Code	Name	Baseline Budget	Potential Budget Revisions	Approved Budget Revisions	Current Budget	Original Downstream Contract	Potential Contract Changes	Approved Contract Changes	Projected Cost	Funds Available
	2013902	Farmington High School & Central Office	124,836,478	3,535	234,134	125,074,147	119,728,099	56,615	254,504	120,039,218	5,034,929
	2013902 HS	Farmington High School	121,853,805	3,535	232,705	122,090,045	116,827,801	56,615	253,075	117,137,491	4,952,554
	2 HS	CM Staff, General Conditions & Reimbursables	4,089,019	9,784	0	4,098,803	4,089,018	9,784	0	4,098,802	1
	2000 HS	Staff	3,869,759	0	0	3,869,759	3,869,758	0	0	3,869,758	1
CM Staff			3,869,759	0	0	3,869,759	3,869,758	0	0	3,869,758	1
	2100 HS	General Conditions & Reimbursables	219,260	9,784	0	229,044	219,260	9,784	0	229,044	0
CM GCs & Reimbursables			219,260	9,784	0	229,044	219,260	9,784	0	229,044	0
	8 HS	Trade Contractors	109,351,792	4,513	389,043	109,745,348	109,447,857	47,809	249,682	109,745,348	0
	8000 HS	Trade Contractors	109,351,792	4,513	389,043	109,745,348	109,447,857	47,809	249,682	109,745,348	0
Site Work			12,441,275	-262,950	266,350	12,444,675	12,436,275	-262,950	271,350	12,444,675	0
Concrete			3,724,000	0	0	3,724,000	3,717,300	0	6,700	3,724,000	0
Masonry			6,047,700	0	-23,113	6,024,587	6,047,700	0	-23,113	6,024,587	0
Steel			10,664,100	0	0	10,664,100	10,635,000	0	29,100	10,664,100	0
Metal Fabrications			2,049,000	-13,585	0	2,035,415	2,049,000	-13,585	0	2,035,415	0
Arch Woodwork			4,031,001	-22,946	-73,847	3,934,208	4,031,001	-22,946	-73,847	3,934,208	0
General Trades			6,051,232	48,786	144,352	6,244,370	6,051,232	48,786	144,352	6,244,370	0
Membrane Roofing			3,377,336	0	-70,000	3,307,336	3,377,336	0	-70,000	3,307,336	0
Spray Applied Fireproofing			2,469,000	-1,986	0	2,467,014	2,469,000	-1,986	0	2,467,014	0
Firestopping			153,051	0	3,780	156,831	153,051	0	3,780	156,831	0
Al-Fr Ent Storefront			6,764,513	0	-1,409	6,763,104	6,764,513	0	-1,409	6,763,104	0
Gyp Board			7,798,333	7,947	25,519	7,831,799	7,798,333	7,947	25,519	7,831,799	0
Flooring			2,751,542	0	0	2,751,542	2,751,542	0	0	2,751,542	0
Painting			901,979	-327	0	901,652	901,979	-327	0	901,652	0
Foodservice Equip			1,457,771	0	0	1,457,771	1,457,771	0	0	1,457,771	0
Fire Protection			1,416,000	398	37,119	1,453,517	1,416,000	398	37,119	1,453,517	0
Window Treatments			202,556	0	0	202,556	202,556	0	0	202,556	0
Plumbing			17,315,500	191,144	-75,463	17,431,181	17,317,000	191,144	-76,963	17,431,181	0
HVAC			582,940	0	0	582,940	582,940	0	0	582,940	0

Grouped by WBS. Summarized by Line Item Name.

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Line Item Name	Code	Name	Baseline Budget	Potential Budget Revisions	Approved Budget Revisions	Current Budget	Original Downstream Contract	Potential Contract Changes	Approved Contract Changes	Projected Cost	Funds Available
Electrical			8,394,900	2,068	153,099	8,550,067	8,383,000	2,068	164,999	8,550,067	0
Sitework Enabling			1,667,735	-43,296	0	1,624,439	1,815,000	0	-190,561	1,624,439	0
Final Cleaning			129,600	0	0	129,600	129,600	0	0	129,600	0
Abatement & Demolition			2,353,087	-37,900	0	2,315,187	2,353,087	-37,900	0	2,315,187	0
Masonry Reno			95,000	0	0	95,000	95,000	0	0	95,000	0
Unassigned			696,400	0	0	696,400	696,400	0	0	696,400	0
Waterproofing			387,007	0	0	387,007	387,007	0	0	387,007	0
Acoustical			41,158	0	0	41,158	41,158	0	0	41,158	0
Tiling			1,337,376	0	0	1,337,376	1,337,376	0	0	1,337,376	0
Electrical, Low Voltage, Fire Alarm			309,700	0	0	309,700	309,700	0	0	309,700	0
Low Voltage Systems			3,741,000	137,160	2,656	3,880,816	3,741,000	137,160	2,656	3,880,816	0
	9 HS	Bond, Insurance, Allowances, Contingencies & Fees	8,412,994	-10,762	-156,338	8,245,894	3,290,926	-978	3,393	3,293,341	4,952,553
	9000 HS	Bonds & Insurance	1,787,032	-978	3,393	1,789,447	1,787,032	-978	3,393	1,789,447	0
CM GCs & Reimbursables			1,787,032	-978	3,393	1,789,447	1,787,032	-978	3,393	1,789,447	0
	9100 HS	Allowances	1,800,500	0	-145,000	1,655,500	0	0	0	0	1,655,500
Utility Company Charge			265,000	0	0	265,000	0	0	0	0	265,000
Floor Protection Area F			25,000	0	0	25,000	0	0	0	0	25,000
Temp Heat For Masonry			25,000	0	0	25,000	0	0	0	0	25,000
115000 Misc Equipment			25,000	0	-25,000	0	0	0	0	0	0
Firestopping Area F			5,000	0	0	5,000	0	0	0	0	5,000
Fire Shutters in Classrooms			120,000	0	-120,000	0	0	0	0	0	0
Wood Stair and Platforms			110,000	0	0	110,000	0	0	0	0	110,000
Laboratory Safety Devices			60,000	0	0	60,000	0	0	0	0	60,000
Floors Boxes Area F			65,000	0	0	65,000	0	0	0	0	65,000
Sitework Tennis Court			1,100,500	0	0	1,100,500	0	0	0	0	1,100,500
	9200 HS	Contingencies	3,321,570	-9,784	-14,731	3,297,055	0	0	0	0	3,297,055

Grouped by WBS. Summarized by Line Item Name.

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Line Item Name	Code	Name	Baseline Budget	Potential Budget Revisions	Approved Budget Revisions	Current Budget	Original Downstream Contract	Potential Contract Changes	Approved Contract Changes	Projected Cost	Funds Available
CM Contingency			3,321,570	-9,784	-14,731	3,297,055	0	0	0	0	3,297,055
	9300 HS	Fees	1,503,892	0	0	1,503,892	1,503,894	0	0	1,503,894	-2
CM Fee			1,503,892	0	0	1,503,892	1,503,894	0	0	1,503,894	-2
	2013902 CO	Central Office	2,982,673	0	1,429	2,984,102	2,900,298	0	1,429	2,901,727	82,375
	2 CO	CM Staff, General Conditions & Reimbursables	191,151	0	0	191,151	191,151	0	0	191,151	0
	2000 CO	Staff	185,716	0	0	185,716	185,716	0	0	185,716	0
CM Staff			185,716	0	0	185,716	185,716	0	0	185,716	0
	2100 CO	General Conditions & Reimbursables	5,435	0	0	5,435	5,435	0	0	5,435	0
CM GCs & Reimbursables			5,435	0	0	5,435	5,435	0	0	5,435	0
	8 CO	Trade Contractors	2,627,531	0	1,426	2,628,957	2,627,531	0	1,426	2,628,957	0
	8000 CO	Trade Contractors	2,627,531	0	1,426	2,628,957	2,627,531	0	1,426	2,628,957	0
Final Cleaning			8,400	0	0	8,400	8,400	0	0	8,400	0
Abatement & Demolition			41,913	0	0	41,913	41,913	0	0	41,913	0
Concrete			22,700	0	0	22,700	22,700	0	0	22,700	0
Masonry			105,000	0	0	105,000	105,000	0	0	105,000	0
Structural Steel			22,000	0	0	22,000	22,000	0	0	22,000	0
3.11 Millwork and Casework			71,799	0	0	71,799	71,799	0	0	71,799	0
Waterproofing			6,893	0	0	6,893	6,893	0	0	6,893	0
Firestopping			2,726	0	0	2,726	2,726	0	0	2,726	0
Roofing			471,664	0	0	471,664	471,664	0	0	471,664	0
Alum Ent, Strfrnt, Cwall, Metal Siding			120,487	0	0	120,487	120,487	0	0	120,487	0
Acoustical			45,490	0	0	45,490	45,490	0	0	45,490	0
Drywall & Acoustical			138,902	0	0	138,902	138,902	0	0	138,902	0
Flooring			49,009	0	0	49,009	49,009	0	0	49,009	0
Painting			16,066	0	0	16,066	16,066	0	0	16,066	0
Tiling			23,821	0	0	23,821	23,821	0	0	23,821	0
General Trades			170,468	0	0	170,468	170,468	0	0	170,468	0
Window Treatments			3,608	0	0	3,608	3,608	0	0	3,608	0
Fire Protection			70,000	0	0	70,000	70,000	0	0	70,000	0

Grouped by WBS. Summarized by Line Item Name.

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Line Item Name	Code	Name	Baseline Budget	Potential Budget Revisions	Approved Budget Revisions	Current Budget	Original Downstream Contract	Potential Contract Changes	Approved Contract Changes	Projected Cost	Funds Available
HVAC			676,560	0	-3,581	672,979	676,560	0	-3,581	672,979	0
Electrical			89,000	0	0	89,000	89,000	0	0	89,000	0
Electrical, Low Voltage, Fire Alarm			342,300	0	5,007	347,307	342,300	0	5,007	347,307	0
Site Work			128,725	0	0	128,725	128,725	0	0	128,725	0
	9 CO	Bond, Insurance, Allowances, Contingencies & Fees	163,991	0	3	163,994	81,616	0	3	81,619	82,375
	9000 CO	Bonds & Insurance	44,319	0	3	44,322	44,319	0	3	44,322	0
CM GCs & Reimbursables			44,319	0	3	44,322	44,319	0	3	44,322	0
	9200 CO	Contingencies	82,375	0	0	82,375	0	0	0	0	82,375
CM Contingency			82,375	0	0	82,375	0	0	0	0	82,375
	9300 CO	Fees	37,297	0	0	37,297	37,297	0	0	37,297	0
CM Fee			37,297	0	0	37,297	37,297	0	0	37,297	0
TOTAL			124,836,478	3,535	234,134	125,074,147	119,728,099	56,615	254,504	120,039,218	5,034,929

Owner Changes Log

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Control Account	Owner CO #	Budget Change
Potential		28,831
CE-062		-264,153
PCO 052 - PR #4 - 1928 Scope Impact for FHS		-264,153
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.		-222,420
024100 - 2.02 - Abatement and Demolition (New HS)- American Env.		-37,900
010815 - Liability Insurances		-2,213
010805 - P&P Bonds		-1,620
CE-069		7,032
PCO 033 - (Returned Submittal) End Curtains with Logo (General Trades)		7,032
069100 - 2.10a - General Trades (New HS) - Scope Construction		6,930
010815 - Liability Insurances		59
010805 - P&P Bonds		43
CE-070		6,107
PCO 034 - (Returned Submittal) Media Center Telescoping Seating Custom Color Carpet (General Trades)		6,107
069100 - 2.10a - General Trades (New HS) - Scope Construction		6,019
010815 - Liability Insurances		51
010805 - P&P Bonds		37
CE-081		-18,265
CM Phase 1 Allowance		-18,265
312315 - 1.01 - SiteWork (New HS) - Gerber Construction, Inc.		-18,000
010815 - Liability Insurances		-153
010805 - P&P Bonds		-112
CE-086		6,903
PCO 032 - RFI #222 AV System: Add (1) Middle Atlantic UPS-2200R- IP (Equipment Rack Power)		6,903
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		4,076
010815 - Liability Insurances		58
010805 - P&P Bonds		42
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		2,727
CE-087		-62,762
PCO 035 - PR #16 Existing Utilities vs Proposed Grading (RFI #194 & RFI #269 RFI #275)		-62,762
055050 - 2.05b - Misc. Metal Steel (New HS) - Shepard Steel		-21,321
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.		19,535
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.		18,456
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.		-78,521
010815 - Liability Insurances		-526
010805 - P&P Bonds		-385
CE-093		28,625
PCO 060 - PR #34 - OT/PT Rooms 1219 & 1221		28,625
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		-2,572
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		0

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical		31,262
210050 - 2.21 - Fire Protection (New HS) - H.H.S Mechanical		596
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		195
064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group		-1,271
010815 - Liability Insurances		240
010805 - P&P Bonds		175
CE-094		46,164
PCO 061 - PR #35 - PE Additions - Ice Machine & Washer/Dryer		46,164
069100 - 2.10a - General Trades (New HS) - Scope Construction		0
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical		35,000
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		10,494
075000 - 2.07n - Membrane Roofing (New HS) - Greenwood Industry		0
010815 - Liability Insurances		387
010805 - P&P Bonds		283
CE-098		0
Central Office Changes - FPS (Forthcoming Proposal Request)		0
069100 - 2.10a - General Trades (New HS) - Scope Construction		0
CE-099		1,336
PCO 040 - (Returned Product Data) Ceiling Mounted Urinal Screens (General Trades)		1,336
069100 - 2.10a - General Trades (New HS) - Scope Construction		1,317
010815 - Liability Insurances		11
010805 - P&P Bonds		8
CE-100		5,908
PCO 044 - RFI #147 & RFI #199 Modified Kiln Vent System (General Trades)		5,908
069100 - 2.10a - General Trades (New HS) - Scope Construction		5,823
010815 - Liability Insurances		49
010805 - P&P Bonds		36
CE-101		95,000
PR#20 - Neutralization Tank (Chem. Labs- None ADA LSK1 Sinks) (RFI #210 & 241, 256) Estimate Material Cost		95,000
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical		95,000
CE-102		-18,019
PCO 046 - PR#19 - Poke Thru Locations & Revisions (Electrical New HS)		-18,019
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		-17,758
010815 - Liability Insurances		-151
010805 - P&P Bonds		-110
CE-104		1,076
PCO 041 - (Returned Submittal) RFI #192 AED Cabinet Misc. Equipment Defibrillator		1,076
069100 - 2.10a - General Trades (New HS) - Scope Construction		1,060
010815 - Liability Insurances		9

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Control Account	Owner CO #	Budget Change
010805 - P&P Bonds		7
CE-108		56,882
PCO 039 - PR #22 Changes in White Boards and Data Drops		56,882
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		57,286
069100 - 2.10a - General Trades (New HS) - Scope Construction		-1,229
010815 - Liability Insurances		476
010805 - P&P Bonds		349
CE-111		8,615
PCO 049 - (Returned Submittal) Communications Racks Frames And Enclosures - Product Data (Low Voltage)		8,615
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		8,490
010815 - Liability Insurances		72
010805 - P&P Bonds		53
CE-116		30,229
PCO 045 - RFI #277 - Stainless Steel Hand Dryers (General Trades RFI # 29)		30,229
069100 - 2.10a - General Trades (New HS) - Scope Construction		29,791
010815 - Liability Insurances		253
010805 - P&P Bonds		185
CE-118		-2,733
PCO 066 - PR#37 - (Returned Submittal) Misc. Metals Cost Credit Auditorium HHS. Wall Framing/Post		-2,733
055050 - 2.05b - Misc. Metal Steel (New HS) - Shepard Steel		-2,693
010815 - Liability Insurances		-23
010805 - P&P Bonds		-17
CE-119		3,000
(Returned Submittal) Alt. Material Substitution (Auditorium Metal Ceiling Panels)		3,000
055050 - 2.05b - Misc. Metal Steel (New HS) - Shepard Steel		3,000
CE-120		1,855
PCO 051 - PR#25 - (RFI #266) AV SR devices added & relocated in Small Group rooms Area A,B (Low Voltage)		1,855
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		1,828
010815 - Liability Insurances		16
010805 - P&P Bonds		11
CE-121		15,075
PCO 059 - PR#26R - Door Hardware Revisions		15,075
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		0
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		6,665
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		8,192
010815 - Liability Insurances		126
010805 - P&P Bonds		92
CE-122		0
FHS - RFI #283 - In Building Cellular Amplification (Forthcoming PR)		0
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		0
CE-123		22,038

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
PCO 067 - (ASI-17) Commercial Showers & Basins Type (SH-3) Provide SH1-Non ADA w/ Full Enclosure		22,038
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical		21,718
069100 - 2.10a - General Trades (New HS) - Scope Construction		0
010815 - Liability Insurances		185
010805 - P&P Bonds		135
CE-124		0
RFI #299 - Extra Window Heads Vs. Window Shade (Fire Shutter Fix)		0
210050 - 2.21 - Fire Protection (New HS) - H.H.S Mechanical		0
CE-125		2,014
PCO 046 - RFI #281 Auto Shop Welding Curtain Discrepancy		2,014
069100 - 2.10a - General Trades (New HS) - Scope Construction		1,985
010815 - Liability Insurances		17
010805 - P&P Bonds		12
CE-126		31,255
PCO 063 - PR#23 - Revisions to power & data outlets per furniture layout		31,255
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		5,000
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		25,801
010815 - Liability Insurances		262
010805 - P&P Bonds		192
CE-127		-212
Applying -to-Trade Allowance - RFI #265 & RFI #335 - Drop Ceiling to Hard Ceiling (Area E, 2nd Floor) Dimmer Rm 2555 -		-212
078100 - 2.07s, 2.09a, - Spray Applied Fireproofing/ Acoustical (New HS) - H.Carr & Son		-1,986
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		1,775
010815 - Liability Insurances		-2
010805 - P&P Bonds		1
CE-129		0
RFI #310 - Step 2479 - Washer Connection (Ferguson Mechanical)		0
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical		0
CE-132		7,538
PCO 055 - RFI #329 - Stair 5 Ramp Rail Approval Comments (SKA-057)		7,538
055050 - 2.05b - Misc. Metal Steel (New HS) - Shepard Steel		7,429
010815 - Liability Insurances		63
010805 - P&P Bonds		46
CE-133		-332
Applying -to- Trade Allowance - PR #31 - Wood & Hollow Metal Door Changes		-332
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		0
099110 - 2.09p - Painting (New HS) - MacKenzie Service Corp.		-327
010815 - Liability Insurances		-3

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Control Account	Owner CO #	Budget Change
010805 - P&P Bonds		-2
CE-134		0
Digital Signage Displays per Owners' Request (Owner's Request Forthcoming PR)		0
069100 - 2.10a - General Trades (New HS) - Scope Construction		0
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		0
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		0
CE-135		-1,126
PCO 068 - PR#36 - Deletion of Cubicle Curtains & Track in Trainer's Office -Room 1441		-1,126
069100 - 2.10a - General Trades (New HS) - Scope Construction		-1,110
010815 - Liability Insurances		-9
010805 - P&P Bonds		-7
CE-136		34,728
PCO 050 - PR #28 - Camera Type Change Security Advanced Featured Multi-Unit (Low- Voltage)		34,728
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		34,224
010815 - Liability Insurances		291
010805 - P&P Bonds		213
CE-137		-1,800
PR#29 - Changes to tack board size, power, data & HDMI elevation update in Wood & Auto Shop		-1,800
069100 - 2.10a - General Trades (New HS) - Scope Construction		-1,800
CE-138		0
PR#30R - Roof Access Light Fixture Revisions (Revised PR to Re-allocate Fixtures in New HS)		0
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		0
CE-139		-20,662
PCO 054 - PR #33 - Main office Room #1321 - Millwork Desk Removals (1st Floor Area C)		-20,662
064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group		-20,362
010815 - Liability Insurances		-173
010805 - P&P Bonds		-127
CE-141		11,010
PCO #057 Door & Hardware Review Comments (Return Submittals)		11,010
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		10,850
010815 - Liability Insurances		92
010805 - P&P Bonds		68
CE-142		0
Added Key Punch 500- Key Banks (Owner's Request Forthcoming PR)		0
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		0
CE-143		-4,086
PCO 064 -RFI #352 - Additional Classroom Elevations (Changed Wall Types- Cost Credit Area A)		-4,086
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		-4,027

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
010815 - Liability Insurances		-34
010805 - P&P Bonds		-25
CE-147		591
PCO 058 - PR #27R - Library/Media - Work Room #2410 Revision		591
210050 - 2.21 - Fire Protection (New HS) - H.H.S Mechanical		-198
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		1,605
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.		-1,405
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.		-6,271
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical		8,164
064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group		-1,313
010815 - Liability Insurances		5
010805 - P&P Bonds		4
CE-148		0
Re: FHS - RFI #0368 - Submittal Review Appliance Models (SCOPE RFI #35)		0
260050 - 2.26 - Electrical (New HS) - Ferguson Electric		0
069100 - 2.10a - General Trades (New HS) - Scope Construction		0
Approved		234,134
CE-002		110,459
PCO 002 - PR #1 - Track & Field Throwing Area		110,459
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #1	108,856
010815 - Liability Insurances	Owner CO #1	925
010805 - P&P Bonds	Owner CO #1	678
CE-003		11,680
PCO 003 - RFI #51 - Grease Trap & SMH 11		11,680
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #2	11,510
010815 - Liability Insurances	Owner CO #2	98
010805 - P&P Bonds	Owner CO #2	72
CE-048		-30,838
PCO 004 - PR #2 - Footing Drains at Area C & D		-30,838
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #2	-30,390
010815 - Liability Insurances	Owner CO #2	-258
010805 - P&P Bonds	Owner CO #2	-190
CE-049		242,506
PCO 009 - PR #9 - Eversource Revisions Elec Primary		242,506
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #2	172,179
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #2	66,809
010815 - Liability Insurances	Owner CO #2	2,031
010805 - P&P Bonds	Owner CO #2	1,487
CE-050		-54,321
PCO 006 - Cost Savings Credit - UG Strom & Sanitary Cast Iron to PVC (Excludes Grease Waste)		-54,321
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #2	-53,533

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
010815 - Liability Insurances	Owner CO #2	-455
010805 - P&P Bonds	Owner CO #2	-333
CE-051		-18,972
PCO 007 - Cost Savings Credit - Ferguson Plumb. Hangers		-18,972
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #2	-18,697
010815 - Liability Insurances	Owner CO #2	-159
010805 - P&P Bonds	Owner CO #2	-116
CE-052		-31,454
PCO 008 - Cost Savings Credit - Ferguson HVAC Hangers		-31,454
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #2	-30,998
010815 - Liability Insurances	Owner CO #2	-263
010805 - P&P Bonds	Owner CO #2	-193
CE-053		-37,568
PCO 010R - PR #6 - Deletion of Bi-polar Ionization -FHS		-37,568
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #4	-37,023
010815 - Liability Insurances	Owner CO #4	-315
010805 - P&P Bonds	Owner CO #4	-230
CE-054		-3,633
PCO 011 - PR #7 - Deletion of Bi-polar Ionization -BOE		-3,633
230055 - 2.22b, 2.23b - Plumbing & HVAC (Reno -CO)- Performance Plumbing	Owner CO #4	-3,581
0108151 - Liability Insurances	Owner CO #4	-30
0108051 - P&P Bonds	Owner CO #4	-22
CE-055		67,028
PCO 015R - PR #10 Plumbing Revisions (Rework Plumb. Storm Drain Area A Included)		67,028
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #4	2,410
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #4	63,646
010815 - Liability Insurances	Owner CO #4	561
010805 - P&P Bonds	Owner CO #4	411
CE-056		-15,688
PCO 016 - RFI #70 - Additional Fire Wrap		-15,688
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.	Owner CO #3	14,419
078400 - 2.07f - Firestopping (New HS) - Barber Firestop Systems	Owner CO #3	3,780
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #3	-33,660
010815 - Liability Insurances	Owner CO #3	-131
010805 - P&P Bonds	Owner CO #3	-96
CE-057		-71,031
PCO 012 - Cost Savings Credit - Roofing Trade Allowance (NEW HS)		-71,031
075000 - 2.07n - Membrane Roofing (New HS) - Greenwood Industry	Owner CO #2	-70,000
010815 - Liability Insurances	Owner CO #2	-595

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
010805 - P&P Bonds	Owner CO #2	-436
CE-058		106,278
PR #3 - Miscellaneous Equipment (Revised - Item F7.Glassware Washer Final Cost)		106,278
069100 - 2.10a - General Trades (New HS) - Scope Construction	Owner CO #4	132,352
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #4	1,857
400015 - Allowances - 115000 Mics. Equipment	Owner CO #4	-25,000
010815 - Liability Insurances	Owner CO #4	890
010805 - P&P Bonds	Owner CO #4	652
064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group	Owner CO #4	-4,473
CE-059		-84,101
PCO 017 - ASI #11 - Sprinkler System instead of Fire Shutters (RFI #067)		-84,101
210050 - 2.21 - Fire Protection (New HS) - H.H.S Mechanical	Owner CO #3	37,119
400017 - Allowances - Fire Shutters in Classrooms	Owner CO #3	-120,000
010815 - Liability Insurances	Owner CO #3	-704
010805 - P&P Bonds	Owner CO #3	-516
CE-060		6,357
PCO 013 - PR #11 - Carbon Monoxide Detectors		6,357
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #2	6,265
010815 - Liability Insurances	Owner CO #2	53
010805 - P&P Bonds	Owner CO #2	39
CE-061		-74,277
PCO 014 - Cost Savings Credit - VE_Display Case & Grade 1 Locks		-74,277
064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group	Owner CO #2	-73,200
010815 - Liability Insurances	Owner CO #2	-622
010805 - P&P Bonds	Owner CO #2	-455
CE-063		39,436
PCO 025 - PR #8R - Eyewash covers with electric alarm notification		39,436
220050 - 2.22a - Plumbing & HVAC (New HS) - Ferguson Mechanical	Owner CO #5	34,802
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #5	4,062
010815 - Liability Insurances	Owner CO #5	330
010805 - P&P Bonds	Owner CO #5	242
CE-065		-14,104
PCO 019 - 18ga Metal Stud Backup (Alt.,5)		-14,104
040050 - 204a - Masonry (New HS) - CT. Mason	Owner CO #3	-25,000
092950 - 2.09c - Gypsum Board/Drywall (New HS) - GDS Contracting Corp.	Owner CO #3	11,100
010815 - Liability Insurances	Owner CO #3	-118
010805 - P&P Bonds	Owner CO #3	-86
CE-066		21,277
PCO 022 - PR#14 - Flagpole Lighting (RFI #208)		21,277
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #4	17,934
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #4	3,035

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
010815 - Liability Insurances	Owner CO #4	178
010805 - P&P Bonds	Owner CO #4	130
CE-082		23,069
PCO 023 - PR#15 Auditorium Movable Lighting		23,069
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #4	22,735
010815 - Liability Insurances	Owner CO #4	193
010805 - P&P Bonds	Owner CO #4	141
CE-084		1,666
PCO 030 - RFI #161 AV System Volume Control (Low Voltage)		1,666
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.	Owner CO #5	1,642
010815 - Liability Insurances	Owner CO #5	14
010805 - P&P Bonds	Owner CO #5	10
CE-085		1,029
PCO 031 - RFI #172 AV System; QSC Core 110f Discontinued (Low Voltage)		1,029
280050 - 2.27 - Low Voltage (New HS) - Anderson Electrical Contr.	Owner CO #5	1,014
010815 - Liability Insurances	Owner CO #5	9
010805 - P&P Bonds	Owner CO #5	6
CE-088		485
PCO 028 - PR#17 Changes to Curtain Wall in Area C (RFI # 202 & 203)		485
040050 - 204a - Masonry (New HS) - CT. Mason	Owner CO #4	1,887
084113 - 2.08 - Al-Fr Ent Storefront, Curtainwall (New HS) - Lockheed Arch. Solutions	Owner CO #4	-1,409
010815 - Liability Insurances	Owner CO #4	4
010805 - P&P Bonds	Owner CO #4	3
CE-090		-547
PCO 027 - PR#13 Revisions to typical classroom casework		-547
064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group	Owner CO #4	-539
010815 - Liability Insurances	Owner CO #4	-5
010805 - P&P Bonds	Owner CO #4	-3
CE-091		1,152
PCO 026 - PR#18 Timeclocks in Area D team rooms (RFI #059)		1,152
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #4	-498
069100 - 2.10a - General Trades (New HS) - Scope Construction	Owner CO #4	1,634
010815 - Liability Insurances	Owner CO #4	9
010805 - P&P Bonds	Owner CO #4	7
CE-092		34,434
PCO 029 - PR#21 - Interior Lighting Upgrades (Ferguson Electric.)		34,434
260050 - 2.26 - Electrical (New HS) - Ferguson Electric	Owner CO #5	33,935
010815 - Liability Insurances	Owner CO #5	288
010805 - P&P Bonds	Owner CO #5	211
CE-149		3,812
PCO 018R2 - PR #5 - Car Charging Station Relocation (RFI #032)		3,812
312316 - 2.31 - Sitework (New HS) - J. Iapaluccio, Inc.	Owner CO #4	-1,250

Out-Of Scope

Grouped by Budget Status, Change Event No. and Change Event Name.

Farmington HS

Reporting Period ending 2023-07-27

Cost in USD

Control Account	Owner CO #	Budget Change
260056 - 2.28 - Electrical and Low Voltage (Reno - CO)- Net Services, LLC	Owner CO #4	5,007
0108151 - Liability Insurances	Owner CO #4	32
0108051 - P&P Bonds	Owner CO #4	23
TOTAL		262,965

CM In-Scope Changes Log

Contingency & Allowances

Grouped by Funding Source, Budget Status and Change Event No..

Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Change Event Name	Control Account	Owner CO #	Budget Transfer	Budget Change
CM Contingency			0	0
Potential			0	0
CE-083			0	0
Phase 1 Library Fencing (CM Contingency)	780020 - CM Contingency		0	-9,784
Phase 1 Library Fencing (CM Contingency)	010539 - Miscellaneous Office Expenses		0	9,784
Approved			0	0
CE-067			0	0
PCO 024 - Farmington HS - Add Gas Turrets (FURNISH ONLY)	780020 - CM Contingency	Owner CO #4	0	-4,365
PCO 024 - Farmington HS - Add Gas Turrets (FURNISH ONLY)	064010 - 2.06 - Arch Woodwork/Lab Casework (New HS) - Legere Group	Owner CO #4	0	4,365
CE-071			0	0
PCO 020 - Added Badminton Sleeves & Material Cost Credit for Volleyball Sleeves	069100 - 2.10a - General Trades (New HS) - Scope Construction	Owner CO #5	0	10,366
PCO 020 - Added Badminton Sleeves & Material Cost Credit for Volleyball Sleeves	780020 - CM Contingency	Owner CO #5	0	-10,366
TOTAL			0	0

PCOs Under Review

Grouped by Funding Source.
Reporting Period ending 2023-07-27

Farmington HS

Cost in USD

Contract Change No.	Contract Change Name	Change Event No.	Change Date	Submitted Date	Potential Changes	Days Requested
Owner Contingency					34,052	0
PCO 032	RFI #222 AV System: Add (1) Middle Atlantic UPS-2200R- IP (Equipment Rack Power)	CE-086	7/2/23	8/3/23	6,903	0
PCO 033	(Returned Submittal) End Curtains with Logo	CE-069	7/2/23	7/3/23	7,032	0
PCO 034	(Returned Submittal) Media Center Telescoping Seating Custom Color Carpet	CE-070	7/2/23	7/5/23	6,107	0
PCO 035	PR #16 Existing Utilities vs Proposed Grading (RFI #194 & RFI #269 RFI #275)	CE-087	9/1/23	9/7/23	-62,762	0
PCO 039	PR #22 Changes in White Boards and Data Drops	CE-108	9/1/23	9/6/23	56,882	0
PCO 040	(Returned Product Data) Ceiling Mounted Urinal Screens (General Trades)	CE-099	7/12/23	8/4/23	1,336	0
PCO 041	(Returned Submittal) RFI #192 AED Cabinet Misc. Equipment Defibrillator	CE-104	7/12/23	8/4/23	1,076	0
PCO 044	RFI #147 & RFI #199 Modify Kiln Vent System (General Trades)	CE-100	9/1/23	9/6/23	5,908	0
PCO 045	RFI #277 - Added Stainless Steel Hand Dryers	CE-116	8/4/23	8/4/23	30,229	0
PCO 046	RFI #281 Auto Shop Welding Curtain Discrepancy	CE-125	9/1/23	9/6/23	2,014	0
PCO 048	PR#19 - Poke Thru Locations & Revisions (Electrical New HS)	CE-102	8/21/23	8/21/23	-18,019	0
PCO 049	(Returned Submittal) Communications Racks Frames And Enclosures - Product Data (Low Voltage)	CE-111	8/31/23	9/6/23	8,615	0
PCO 051	PR#25 - (RFI #266) AV SR devices added & relocated in Small Group rooms Area A,B (Low Voltage)	CE-120	8/31/23	9/6/23	1,855	0
PCO 054	PR #33 - Main office Room #1321 - Millwork Desk Removals (1st Floor Area C)	CE-141	9/1/23	9/6/23	-20,662	0
PCO 055	RFI #329 - Stair 5 Ramp Rail Approval Comments (SKA-057)	CE-132	8/28/23	8/28/23	7,538	0
TOTAL					34,052	0

Farmington High School
O&G Project No. 2013902
August 2023
Monthly Report

Cost/Schedule Impact Items

Below is a listing of current construction/financial issues that may become an impediment to the timely completion of various work items and overall project completion.

- **Schedule**
 - Currently, no significant cost or schedule impacts.
- **Coordination**
 - Currently, no significant cost or schedule impacts.
- **Submittals**
 - Currently, no significant cost or schedule impacts.
- **Request for Information (RFIs)**
 - Currently, no significant cost or schedule impacts.
- **Construction**
 - Currently, no significant cost or schedule impacts.

Farmington High School
O&G Project No. 2013902
August 2023
Monthly Report

Project Commentary

Sitework Activities

- Granite curbing on Monteith Drive started on the center islands.
- Underground Detentions System #124 (west side) installation in progress.

New High School Building

- Building A – Classroom Wing:
 - Ground Face CMU at Stair #1 nearing completion. Stair installation to follow.
 - Drywall installation and taping near complete 2nd and 3rd floors with first coat painting starting.
 - Window installation is nearing completion.
 - Locker installation complete first and second floors.
 - Rooftop RTU curbs delivered and installation started with wood blocking.
- Building B – Classroom Wing:
 - Masonry Brick Veneer nearing completion.
 - Drywall and taping in progress 2nd and 3rd floors.
 - Rooftop RTU curb preparation started.
- Building C – Tech Ed/STEAM Classrooms:
 - Interior Wall Framing is complete on the 2nd floor.
 - CMU installation interior shop classrooms complete. Brick veneer starting
 - CMU in progress in Alt HS and Corridor Areas.
 - MEP rough installation in progress.
- Building D – Kitchen/Gymnasium Areas:
 - Sawtooth skylight welding and acoustical decking complete.
 - Slab on grade concrete placement for cafeteria area complete.
 - Roofing and Skylight Gable Roofing to start.
 - Exterior and Interior CMU walls in progress.
 - Concrete stepped seating complete.
- Building E – Auditorium/Administration Areas
 - Concrete placement in Auditorium seating area in progress.
 - Exterior vapor barrier in progress.
 - Roofing complete on upper roof with mid-roof nearing completion.
 - Interior framing and CMU walls in progress.

Mechanical/Electrical/Plumbing Coordination

- BIM Coordination Complete for High School project.
- Area F (900-wing) – Coordination to begin with Reno Contractors. On hold for Owner requested room layout changes. Coordination to commence in September once design documents received.



09/14/2023

Progress Schedule Update Narrative

Project # 2019302
 Farmington High School
 10 Monteith Drive
 Farmington CT 06032

Schedule Update #09

Base Contract Duration of Phase 2:	630
Current Approved Duration of Phase 2:	630
Difference in Contract Days:	0
Days Lapsed Since NTP:	307
Days Remaining to Final Project Completion:	323
Percentage of Days Expended:	48.73%
Actual Physical Progress:	48.74%

Baseline Milestones			
	Baseline	Current Update	Difference
MIL.1500 Phase 1 Work Commence Early Enabling	07/11/2022	07/11/22	-
MIL.1010 Complete Phase 1 Early Enabling	08/24/2022	08/24/2022	-
MIL.1020 Start Phase 2 Work Onsite	11/08/2022	11/08/2022	-
MOBP2.1000 Commence Phase 2	11/08/2022	11/08/2022	-
MIL.1050 Complete Existing Building Abatement / Demo & Renovations	11/05/2024	10/16/2024	+14
MIL.1060 Complete Construction – Central Office	05/01/2025	02/14/2025	+53
MIL.1080 Overall Project Complete	07/03/2025	07/01/2025	+2



Newly Added as of Update 07 DD 09/09/2023			
MIL.1520 Area A Construction Complete	04/09/2024	04/22/2024	-9
MIL.1530 Area B Construction Complete	05/07/2024	05/24/2024	-14
MIL.1540 Area C Construction Complete	06/05/2024	06/04/2024	+1
MIL.1550 Area D Construction Complete	07/11/2024	07/10/2024	+1
MIL.1560 Area E Construction Complete	07/30/2024	07/25/2024	+9

Narration of Work:

Area E concrete continues in the auditorium with stepped seating. Skylight detailing is complete. Area A painting has started with ceiling grid starting in September. The exterior brick veneer is near complete on Area B. Windows are near complete in Area A, including installation of glass. Area C masonry block is nearing completion, both interior and exterior. Area D blockwork started. Roofing near complete all areas of the building. The north parking lot has been paved. Curbing installation started along Montieth Drive.

Description of Critical:

The critical path is shown as the procurement and installation of the switchgear and the construction of each electrical room. Finish work (flooring and paint) and casework though all areas are also shown on the critical path.



Changes to Schedule

Added & Deleted Activities:

The following Activities have been added to the project	
Activity ID	Activity Name
CHG.1050	PR#35, Ice Maker & Washer Dryer 1421
CHG.1060	PR#34, Delete OT/PT Office
CHG.1070	PR#27R, Changes to Media Center
EXTE.1180	Install Glass and Glazing, Area E
EXTD.1180	Install Glass and Glazing, Area D
EXTC.1180	Install Glass and Glazing, Area C
EXTA.1210	Install Glass and Glazing, Area A
INT1D.3760	Install Skyfold Operable Partition, Area D LG Gym First Floor
MIL.1110	Permanent Power
CLO.1080	Cutover of Temporary Power
INT1E.2890	Install CMU Walls, Area E Auditorium
INT3A.1810	Install Curtainwall at Stair 1, Area A
INT3B.1810	Install Curtainwall at Stair 2, Area B
INT3B.1820	Install Glazing Stair 2, Area B
INT3A.1820	Install Glazing Stair 1, Area A
INT3B.1830	Install Stair 2 Ceilings & Finishes, Area B
INT3A.1830	Install Stair 1 Ceilings & Finishes, Area A
INT1D.3770	Install CMU Partitions, First Floor Area D Kitchen & Servery
INT1D.1800	Install Wall Tile, Area D
EXTC.1230	Install Sawtooth Skylight Roofing, Area C
EXTC.1240	Install Sawtooth Skylight, Area C
EXTE.1190	Install Sawtooth Skylight Roofing, Area E Roof
EXTE.1200	Install Sawtooth Skylight, Area E Roof
EXTA.1190	Install Metal Panels, Area A
EXTB.1180	Install Metal Panels, Area B
EXTC.1190	Install Metal Panels, Area C



EXTD.1190	Install Metal Panels, Area D
EXTE.1210	Install Metal Panels, Area E
INT1E.1780	Install Stage Flooring, First Floor Area E Auditorium
INT1E.1790	Install Millwork Upper Works, Area E Auditorium
INT1E.1800	Install Metal Ceilings, Area E Auditorium
INT1E.2900	Apply Paint Upper Works, First Floor Area E
CHG.1080	PR#34 OT/PT Office Impacting Completion of Drywall Area B, 1st Floor Area B
CHG.1090	PR#35 Added Washer & Dryer at Athletic Storage Room, 1st Floor Area D

The following Activities have been deleted from the project	
Activity ID	Activity Name
EXTE.1080	Install Lightning Protection, Area E Roof
EXTD.1080	Install Lightning Protection, Area D Roof
EXTC.1080	Install Lightning Protection, Area C Roof

Added & Deleted WBS's:

The following Activities have been deleted from the project	
Activity ID	Activity Name
EXTE.1080	Install Lightning Protection, Area E Roof
EXTD.1080	Install Lightning Protection, Area D Roof
EXTC.1080	Install Lightning Protection, Area C Roof



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 1 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Farmington High School and Central Office						01-Jul-25, P																							
MILESTONES						01-Jul-25, M																							
CONSTRUCTION START & COMPLETION						01-May-25, CONSTRUCT																							
MIL.1110	Permanent Power	0		19-Apr-24	112	◆ Permanent Power																							
MIL.1520	Area A Construction Complete	0		22-Apr-24*	-9	◆ Area A Construction Complete																							
MIL.1530	Area B Construction Complete	0		24-May-24*	-14	◆ Area B Construction Complete																							
MIL.1540	Area C Construction Complete	0		04-Jun-24*	1	◆ Area C Construction Complete																							
MIL.1030	Start Central Office Abatement / Demolition & Renovations	0	20-Jun-24*		0	◆ Start Central Office Abatement / Demolition & Renovations																							
MIL.1550	Area D Construction Complete	0		10-Jul-24*	1	◆ Area D Construction Complete																							
MIL.1560	Area E Construction Complete	0		25-Jul-24*	9	◆ Area E Construction Complete																							
MIL.1100	Substantial Completion - New HS	0		08-Aug-24*	0	◆ Substantial Completion - New HS																							
MIL.1050	Complete Existing Building Abatement / Demolition & Renovations	0		16-Oct-24*	14	◆ Complete Existing Building Abatement / Demolition & Renovations																							
MIL.1060	Complete Construction - Central Office	0		14-Feb-25*	53	◆ Complete Construction - Central Office																							
MIL.1070	Complete Sitework	0		01-May-25*	0	◆ Complete Sitework																							
CLOSE-OUT						01-Jul-25, C																							
MIL.1080	Project Complete	0		01-Jul-25	0	◆ Project Com																							
SUBMITTALS						15-Apr-24, SUBMITTALS																							
DIVISION 02 - EXISTING CONDITIONS						09-Oct-23, DIVISION 02 - EXISTING CONDITIONS																							
SUB.1090	Submit Asbestos Abatement	15	11-Sep-23	25-Sep-23	631	Submit Asbestos Abatement																							
SUB.1060	Submit Selective Demolition	15	11-Sep-23	25-Sep-23	631	Submit Selective Demolition																							
SUB.1000	Submit Building Demolition	15	11-Sep-23	25-Sep-23	631	Submit Building Demolition																							
SUB.1100	Review Asbestos Abatement	14	26-Sep-23	09-Oct-23	631	Review Asbestos Abatement																							
SUB.1070	Review Selective Demolition	14	26-Sep-23	09-Oct-23	631	Review Selective Demolition																							
SUB.1010	Review Building Demolition	14	26-Sep-23	09-Oct-23	631	Review Building Demolition																							
DIVISION 06 - WOOD, PLASTIC & COMPOSITES						12-Nov-23, DIVISION 06 - WOOD, PLASTIC & COMPOSITES																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 2 of: 60
Current Date: 14-Sep-23
BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
SUB.1400	Procure Architectural Woodwork	63	20-Mar-23 A	12-Nov-23	37	Procure Architectural Woodwork																							
DIVISION 08 - OPENINGS		125	03-Apr-23 A	19-Nov-23	410	19-Nov-23, DIVISION 08 - OPENINGS																							
SUB.1670	Procure Fire-Rated Steel Curtain Wall	30	03-Apr-23 A	10-Oct-23	630	Procure Fire-Rated Steel Curtain Wall																							
SUB.1710	Procure Metal Framed Skylights	70	05-May-23 A	19-Oct-23	104	Procure Metal Framed Skylights																							
SUB.1700	Procure Unit Skylights	70	15-May-23 A	19-Nov-23	590	Procure Unit Skylights																							
SUB.1580	Procure Overhead Coiling Doors	42	15-May-23 A	22-Oct-23	144	Procure Overhead Coiling Doors																							
SUB.1550	Procure Doors & Door Hardware	84	30-Jun-23 A	09-Nov-23	134	Procure Doors & Door Hardware																							
DIVISION 09 - FINISHES		100	03-Jul-23 A	25-Oct-23	179	25-Oct-23, DIVISION 09 - FINISHES																							
SUB.1910	Procure Wood Panel Ceiling	30	03-Jul-23 A	10-Oct-23	49	Procure Wood Panel Ceiling																							
SUB.1880	Procure Sheet Carpeting	30	14-Jul-23 A	10-Oct-23	86	Procure Sheet Carpeting																							
SUB.1850	Procure Tiles	30	28-Jul-23 A	10-Oct-23	91	Procure Tiles																							
SUB.1800	Submit Wood Athletic Flooring	1	11-Sep-23	11-Sep-23	179	Submit Wood Athletic Flooring																							
SUB.1810	Review Wood Athletic Flooring	14	12-Sep-23	25-Sep-23	179	Review Wood Athletic Flooring																							
SUB.1820	Procure Wood Athletic Flooring	30	26-Sep-23	25-Oct-23	179	Procure Wood Athletic Flooring																							
DIVISION 10 - SPECIALTIES		176	16-Feb-23 A	29-Oct-23	611	29-Oct-23, DIVISION 10 - SPECIALTIES																							
SUB.2170	Review Site Signage	14	16-Feb-23 A	24-Sep-23	530	Review Site Signage																							
SUB.2320	Review Ground Set Flagpoles	14	04-Apr-23 A	24-Sep-23	530	Review Ground Set Flagpoles																							
SUB.2240	Procure Bathroom Accessories	30	01-Jun-23 A	10-Oct-23	114	Procure Bathroom Accessories																							
SUB.2210	Procure Toilet Compartments	30	01-Jun-23 A	10-Oct-23	107	Procure Toilet Compartments																							
SUB.2140	Review Display Cases	14	20-Jun-23 A	24-Sep-23	56	Review Display Cases																							
SUB.2120	Procure Visual Display Units & Surfaces	49	10-Jul-23 A	29-Oct-23	87	Procure Visual Display Units & Surfaces																							
SUB.2270	Procure Fire Protection Specialties	30	07-Aug-23 A	10-Oct-23	630	Procure Fire Protection Specialties																							
SUB.2330	Procure Ground Set Flagpoles	30	25-Sep-23	24-Oct-23	530	Procure Ground Set Flagpoles																							
SUB.2180	Procure Site Signage	30	25-Sep-23	24-Oct-23	530	Procure Site Signage																							
SUB.2150	Procure Display Cases	30	25-Sep-23	24-Oct-23	56	Procure Display Cases																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 3 of: 60
Current Date: 14-Sep-23
BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
DIVISION 11 - EQUIPMENT		178	10-May-23 A	08-Nov-23	601	08-Nov-23, DIVISION 11 - EQUIPMENT																							
SUB.2450	Procure Residential Appliances	30	10-May-23 A	10-Oct-23	630	Procure Residential Appliances																							
SUB.2420	Procure Loading Dock Equipment	30	15-May-23 A	10-Oct-23	630	Procure Loading Dock Equipment																							
SUB.2510	Procure Laboratory Fume Hoods	30	26-May-23 A	10-Oct-23	97	Procure Laboratory Fume Hoods																							
SUB.2480	Procure Food Service Equipment	30	30-May-23 A	10-Oct-23	224	Procure Food Service Equipment																							
SUB.2630	Procure Gymnasium Dividers	30	03-Jul-23 A	10-Oct-23	163	Procure Gymnasium Dividers																							
SUB.2600	Procure Gymnasium Equipment	30	03-Jul-23 A	10-Oct-23	163	Procure Gymnasium Equipment																							
SUB.2540	Procure Stage Accessories, Draperies & Rigging	30	07-Jul-23 A	10-Oct-23	273	Procure Stage Accessories, Draperies & Rigging																							
SUB.2670	Submit Tennis Equipment	15	11-Sep-23	25-Sep-23	519	Submit Tennis Equipment																							
SUB.2640	Submit Ballfield Equipment	15	11-Sep-23	25-Sep-23	601	Submit Ballfield Equipment																							
SUB.2550	Submit Orchestra Shell	15	11-Sep-23	25-Sep-23	601	Submit Orchestra Shell																							
SUB.2680	Review Tennis Equipment	14	26-Sep-23	09-Oct-23	519	Review Tennis Equipment																							
SUB.2650	Review Ballfield Equipment	14	26-Sep-23	09-Oct-23	601	Review Ballfield Equipment																							
SUB.2560	Review Orchestra Shell	14	26-Sep-23	09-Oct-23	601	Review Orchestra Shell																							
SUB.2690	Procure Tennis Equipment	30	10-Oct-23	08-Nov-23	519	Procure Tennis Equipment																							
SUB.2660	Procure Ballfield Equipment	30	10-Oct-23	08-Nov-23	601	Procure Ballfield Equipment																							
SUB.2570	Procure Orchestra Shell	30	10-Oct-23	08-Nov-23	601	Procure Orchestra Shell																							
DIVISION 12 - FURNISHINGS		173	23-Feb-23 A	10-Oct-23	239	10-Oct-23, DIVISION 12 - FURNISHINGS																							
SUB.2900	Procure Telescoping Seating	30	23-Feb-23 A	10-Oct-23	239	Procure Telescoping Seating																							
SUB.2810	Procure Laboratory Caseworks	30	11-Apr-23 A	10-Oct-23	70	Procure Laboratory Caseworks																							
SUB.2870	Procure Fixed Audience Seating	30	01-Aug-23 A	10-Oct-23	236	Procure Fixed Audience Seating																							
SUB.2780	Procure Roller Window Shades	30	11-Aug-23 A	10-Oct-23	107	Procure Roller Window Shades																							
DIVISION 14 - CONVEYING SYSTEM		91	20-Mar-23 A	10-Dec-23	29	10-Dec-23, DIVISION 14 - CONVEYING SYSTEM																							
SUB.2930	Procure Electric Traction Elevators	91	20-Mar-23 A	10-Dec-23	29	Procure Electric Traction Elevators																							
DIVISION 22 - PLUMBING		30	20-Mar-23 A	10-Oct-23	121	10-Oct-23, DIVISION 22 - PLUMBING																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
SUB.3200	Procure Drinking Fountains	30	20-Mar-23 A	10-Oct-23	121	Procure Drinking Fountains																							
SUB.3170	Procure Commercial Water Closets, Urinals, Lavatories, & Sinks	30	20-Mar-23 A	10-Oct-23	106	Procure Commercial Water Closets, Urinals, Lavatories, & Sinks																							
DIVISION 23 - HEATING, VENTILATING & AIR CONDITIONING		250	20-Mar-23 A	15-Apr-24	308	15-Apr-24, DIVISION 23 - HEATING, VENTILATING & AIR CONDITIONING																							
SUB.4060	Procure DOAS	140	20-Mar-23 A	13-Oct-23	435	Procure DOAS																							
SUB.4050	Procure RTU	196	20-Mar-23 A	04-Jan-24	61	Procure RTU																							
SUB.3440	Procure Laboratory Airflow Controllers	30	01-Aug-23 A	10-Oct-23	97	Procure Laboratory Airflow Controllers																							
SUB.3410	Procure Condensing Boilers	30	01-Aug-23 A	10-Oct-23	630	Procure Condensing Boilers																							
SUB.3530	Procure Valance Cooling & Heating Units	30	07-Aug-23 A	10-Oct-23	630	Procure Valance Cooling & Heating Units																							
SUB.3500	Procure Split-System Air Conditioners	30	07-Aug-23 A	10-Oct-23	630	Procure Split-System Air Conditioners																							
SUB.3380	Procure Diffusers, Registers & Grilles	30	07-Aug-23 A	10-Oct-23	114	Procure Diffusers, Registers & Grilles																							
SUB.3270	Submit Commissioning of HVAC	1	11-Sep-23	11-Sep-23	645	Submit Commissioning of HVAC																							
SUB.4260	Procure RTU 14 Area E	0		11-Sep-23*	142	Procure RTU 14 Area E																							
SUB.3280	Review Commissioning of HVAC	14	12-Sep-23	25-Sep-23	645	Review Commissioning of HVAC																							
SUB.4200	Procure RTU 13 Area D	0		27-Nov-23*	59	Procure RTU 13 Area D																							
SUB.4220	Procure RTU 01 Area D	0		27-Nov-23*	91	Procure RTU 01 Area D																							
SUB.4250	Procure RTU 04 Area D	0		27-Nov-23*	131	Procure RTU 04 Area D																							
SUB.4280	Procure RTU 05 Area E	0		27-Nov-23*	105	Procure RTU 05 Area E																							
SUB.4160	Procure RTU 10 Area A	0		18-Dec-23*	-9	Procure RTU 10 Area A																							
SUB.4170	Procure RTU 09 Area B	0		22-Dec-23*	27	Procure RTU 09 Area B																							
SUB.4210	Procure RTU 11 Area D	0		15-Apr-24*	19	Procure RTU 11 Area D																							
SUB.4240	Procure RTU 02 Area D	0		15-Apr-24*	41	Procure RTU 02 Area D																							
SUB.4270	Procure RTU 06 Area E	0		15-Apr-24*	26	Procure RTU 06 Area E																							
SUB.4290	Procure RTU 12 Area E	0		15-Apr-24*	26	Procure RTU 12 Area E																							
DIVISION 26 - ELECTRICAL		65	09-Feb-23 A	31-Mar-24	59	31-Mar-24, DIVISION 26 - ELECTRICAL																							
SUB.4040	Procure Switchgear	5	09-Feb-23 A	31-Mar-24	59	Procure Switchgear																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 5 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
SUB.4150	Procure Panelboards	5	09-Feb-23 A	31-Mar-24	-21	Procure Panelboards																							
SUB.3620	Procure Digital, Addressable Fire Alarm Systems	30	24-Mar-23 A	10-Oct-23	93	Procure Digital, Addressable Fire Alarm Systems																							
SUB.3590	Procure Video Surveillance Systems	30	24-May-23 A	10-Oct-23	93	Procure Video Surveillance Systems																							
SUB.3560	Procure Access Controls Systems	30	24-May-23 A	10-Oct-23	93	Procure Access Controls Systems																							
SUB.3650	Procure Telephone Entry Systems	30	07-Aug-23 A	10-Oct-23	93	Procure Telephone Entry Systems																							
DIVISION 27 - COMMUNICATIONS		131	11-Apr-23 A	10-Oct-23	93	10-Oct-23, DIVISION 27 - COMMUNICATIONS																							
SUB.3740	Procure Intercommunications Paging & Clock Systems	30	11-Apr-23 A	10-Oct-23	64	Procure Intercommunications Paging & Clock Systems																							
SUB.3710	Procure Audio / Video Systems	30	03-Jul-23 A	10-Oct-23	93	Procure Audio / Video Systems																							
SUB.3680	Procure Communications Systems	30	03-Jul-23 A	10-Oct-23	93	Procure Communications Systems																							
DIVISION 28 - ELECTRONIC SAFETY & SECURITY		36	24-May-23 A	10-Oct-23	93	10-Oct-23, DIVISION 28 - ELECTRONIC SAFETY & SECURITY																							
SUB.3860	Procure Video Surveillance	30	24-May-23 A	10-Oct-23	93	Procure Video Surveillance																							
SUB.3800	Procure Access Control Hardware & System	30	24-May-23 A	10-Oct-23	93	Procure Access Control Hardware & System																							
SUB.3770	Procure Safety & Security Systems	30	24-May-23 A	10-Oct-23	93	Procure Safety & Security Systems																							
SUB.3830	Procure Telephone Entry Systems	30	26-May-23 A	10-Oct-23	93	Procure Telephone Entry Systems																							
DIVISION 31 - EARTHWORK		29	11-Sep-23	09-Oct-23	631	09-Oct-23, DIVISION 31 - EARTHWORK																							
SUB.3870	Submit Site Clearing	15	11-Sep-23	25-Sep-23	631	Submit Site Clearing																							
SUB.3880	Review Site Clearing	14	26-Sep-23	09-Oct-23	631	Review Site Clearing																							
DIVISION 32 - EXTERIOR IMPROVEMENTS		59	11-Sep-23	08-Nov-23	515	08-Nov-23, DIVISION 32 - EXTERIOR IMPROVEMENTS																							
SUB.4010	Submit Courtyard / Field Fixtures	15	11-Sep-23	25-Sep-23	456	Submit Courtyard / Field Fixtures																							
SUB.3980	Submit Site Furnishings	15	11-Sep-23	25-Sep-23	515	Submit Site Furnishings																							
SUB.3950	Submit Chain Link Fences & Gates	15	11-Sep-23	25-Sep-23	477	Submit Chain Link Fences & Gates																							
SUB.4020	Review Courtyard / Field Fixtures	14	26-Sep-23	09-Oct-23	456	Review Courtyard / Field Fixtures																							
SUB.3990	Review Site Furnishings	14	26-Sep-23	09-Oct-23	515	Review Site Furnishings																							
SUB.3960	Review Chain Link Fences & Gates	14	26-Sep-23	09-Oct-23	477	Review Chain Link Fences & Gates																							
SUB.4030	Procure Courtyard / Field Fixtures	30	10-Oct-23	08-Nov-23	456	Procure Courtyard / Field Fixtures																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 7 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
ERECTION - AREA A		4	11-Sep-23	14-Sep-23	124	▼ 14-Sep-23, ERECTION - AREA A																							
ERECTA.1080	Apply Finish Paint to Exterior Exposed Steel, Area A	4	11-Sep-23	14-Sep-23	124	■ Apply Finish Paint to Exterior Exposed Steel, Area A																							
ERECTION - AREA B		4	15-Sep-23	20-Sep-23	142	▼ 20-Sep-23, ERECTION - AREA B																							
ERECTB.1110	Apply Finish Paint to Exterior Exposed Steel, Area B	4	15-Sep-23	20-Sep-23	142	■ Apply Finish Paint to Exterior Exposed Steel, Area B																							
ERECTION - AREA C		15	18-Aug-23 A	25-Sep-23	178	▼ 25-Sep-23, ERECTION - AREA C																							
ERECTC.1070	Erect CMU Walls - Stairwells Area C	7	18-Aug-23 A	19-Sep-23	144	■ Erect CMU Walls - Stairwells Area C																							
ERECTC.1110	Apply Finish Paint to Exterior Exposed Steel, Area C	3	21-Sep-23	25-Sep-23	178	■ Apply Finish Paint to Exterior Exposed Steel, Area C																							
ERECTION - AREA D		15	06-Sep-23 A	04-Oct-23	178	▼ 04-Oct-23, ERECTION - AREA D																							
ERECTD.1280	Erect CMU Walls - Stairwells Area D	7	06-Sep-23 A	19-Sep-23	144	■ Erect CMU Walls - Stairwells Area D																							
ERECTD.1250	Apply Finish Paint to Exterior Exposed Steel, Area D	4	26-Sep-23	29-Sep-23	178	■ Apply Finish Paint to Exterior Exposed Steel, Area D																							
ERECTD.1330	Apply Finish Paint to Exterior Exposed Steel, Partial Second Floor Area D	3	02-Oct-23	04-Oct-23	178	■ Apply Finish Paint to Exterior Exposed Steel, Partial Second Floor Area D																							
ERECTION - AREA E		14	11-Sep-23	28-Sep-23	144	▼ 28-Sep-23, ERECTION - AREA E																							
ERECTE.1120	Pour SOD Partial Second Floor, Area E	2	11-Sep-23	12-Sep-23	149	■ Pour SOD Partial Second Floor, Area E																							
ERECTE.1090	Structural Steel Spray on Fireproofing Partial Second Floor Area E	4	11-Sep-23	14-Sep-23	147	■ Structural Steel Spray on Fireproofing Partial Second Floor Area E																							
ERECTE.1080	Apply Finish Paint to Exterior Exposed Steel, Area E	4	11-Sep-23	14-Sep-23	147	■ Apply Finish Paint to Exterior Exposed Steel, Area E																							
ERECTE.1130	Apply Finish Paint to Exterior Exposed Steel, Partial Second Floor Area E	3	15-Sep-23	19-Sep-23	147	■ Apply Finish Paint to Exterior Exposed Steel, Partial Second Floor Area E																							
ERECTE.1050	Erect CMU Walls - Stairwells Area E	7	20-Sep-23	28-Sep-23	144	■ Erect CMU Walls - Stairwells Area E																							
STRUCTURE EXTERIOR - PH.2		107	24-Jul-23 A	18-Dec-23	146	▼ 18-Dec-23, STRUCTURE EXTERIOR - PH.2																							
AREA A EXTERIOR		58	15-Aug-23 A	09-Nov-23	104	▼ 09-Nov-23, AREA A EXTERIOR																							
EXTA.1170	Install Storefront, Area A	10	15-Aug-23 A	22-Sep-23	61	■ Install Storefront, Area A																							
EXTA.1210	Install Glass and Glazing, Area A	10	30-Aug-23 A	22-Sep-23	56	■ Install Glass and Glazing, Area A																							
EXTA.1180	Caulk Exterior Systems, Area A	5	31-Aug-23 A	15-Sep-23	118	■ Caulk Exterior Systems, Area A																							
EXTA.1190	Install Metal Panels, Area A	10	02-Oct-23*	13-Oct-23	93	■ Install Metal Panels, Area A																							
EXTA.1200	Install Metal Coping & Fascia, Area A	5	16-Oct-23	20-Oct-23	93	■ Install Metal Coping & Fascia, Area A																							
AREA A ROOF		44	11-Sep-23	09-Nov-23	104	▼ 09-Nov-23, AREA A ROOF																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 14 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area A MEP's Classrooms & Labs Second Floor		30	18-Sep-23	27-Oct-23	78	▼ 27-Oct-23, Area A MEP's Classrooms & Labs Second Floor																							
INT2A.1100	Install Finish Plumbing, Second Floor Area A Classrooms	10	18-Sep-23	29-Sep-23	91	■ Install Finish Plumbing, Second Floor Area A Classrooms																							
INT2A.1120	Install Sprinkler Heads, Second Floor Area A Classrooms	3	02-Oct-23	04-Oct-23	88	■ Install Sprinkler Heads, Second Floor Area A Classrooms																							
INT2A.1230	Install AV Equipment, Second Floor Area A	3	09-Oct-23	11-Oct-23	83	■ Install AV Equipment, Second Floor Area A																							
INT2A.1190	Install Tele / Data Finishes, Second Floor Area A Classrooms	5	09-Oct-23	13-Oct-23	81	■ Install Tele / Data Finishes, Second Floor Area A Classrooms																							
INT2A.1110	Install Lighting, Second Floor Area A Classrooms	5	09-Oct-23	13-Oct-23	88	■ Install Lighting, Second Floor Area A Classrooms																							
INT2A.1090	Install Mechanical Finishes, Chilled Beams Second Floor Area A Classrooms	5	09-Oct-23	13-Oct-23	78	■ Install Mechanical Finishes, Chilled Beams Second Floor Area A Classrooms																							
INT2A.1770	Install Finish Lab Equipment, Second Floor Area A Classrooms	10	16-Oct-23	27-Oct-23	78	■ Install Finish Lab Equipment, Second Floor Area A Classrooms																							
Area A Finishes Classrooms & Labs Second Floor		122	18-Sep-23	08-Mar-24	-9	▼ 08-Mar-24, Area A Finishes Classrooms & Labs Second Floor																							
INT2A.1130	Install Visual Display Surfaces, Second Floor Area A Classrooms	3	18-Sep-23	20-Sep-23	105	■ Install Visual Display Surfaces, Second Floor Area A Classrooms																							
INT2A.1140	Install Finished Ceilings, Second Floor Area A Classrooms	5	02-Oct-23	06-Oct-23	61	■ Install Finished Ceilings, Second Floor Area A Classrooms																							
INT2A.1240	Install Classroom Casework, First Floor Area A Classrooms	10	18-Jan-24	31-Jan-24	-9	■ Install Classroom Casework, First Floor Area A Classrooms																							
INT2A.1210	Install Finish Flooring, Second Floor Area A Classrooms	10	01-Feb-24	14-Feb-24	-4	■ Install Finish Flooring, Second Floor Area A Classrooms																							
INT2A.1200	Apply Finish Paint, Second Floor Area A Classrooms	5	15-Feb-24	21-Feb-24	-4	■ Apply Finish Paint, Second Floor Area A Classrooms																							
INT2A.1220	Install Interior Signage, Second Floor Area A Classrooms	2	22-Feb-24	23-Feb-24	-4	■ Install Interior Signage, Second Floor Area A Classrooms																							
INT2A.1250	Final Clean Second Floor Area A Classrooms	5	04-Mar-24	08-Mar-24	-9	■ Final Clean Second Floor Area A Classrooms																							
Area A Bathrooms - Second Floor		132	11-Sep-23	15-Mar-24	-9	▼ 15-Mar-24, Area A Bathrooms - Second Floor																							
Area A Rough-in Bathrooms Second Floor		10	18-Sep-23	29-Sep-23	88	▼ 29-Sep-23, Area A Rough-in Bathrooms Second Floor																							
INT2A.1630	Apply Prime Paint, Second Floor Area A Bathrooms	5	18-Sep-23	22-Sep-23	88	■ Apply Prime Paint, Second Floor Area A Bathrooms																							
INT2A.1570	Frame Ceilings, Second Floor Area A Bathrooms	5	25-Sep-23	29-Sep-23	88	■ Frame Ceilings, Second Floor Area A Bathrooms																							
INT2A.1650	Perform Overhead Inspection, Second Floor Area A Bathrooms	0		29-Sep-23	88	◆ Perform Overhead Inspection, Second Floor Area A Bathrooms																							
Area A MEP's Bathrooms Second Floor		7	02-Oct-23	10-Oct-23	96	▼ 10-Oct-23, Area A MEP's Bathrooms Second Floor																							
INT2A.1610	Install Sprinkler Heads, Second Floor Area A Bathrooms	3	02-Oct-23	04-Oct-23	97	■ Install Sprinkler Heads, Second Floor Area A Bathrooms																							
INT2A.1600	Install Lighting, Second Floor Area A Bathrooms	5	04-Oct-23	10-Oct-23	96	■ Install Lighting, Second Floor Area A Bathrooms																							
INT2A.1590	Install Mechanical Finishes, Chilled Beams Second Floor Area A Bathrooms	2	04-Oct-23	05-Oct-23	99	■ Install Mechanical Finishes, Chilled Beams Second Floor Area A Bathrooms																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 15 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area A Finishes Bathrooms Second Floor		132	11-Sep-23	15-Mar-24	-9	15-Mar-24, Area A Finishes Bathrooms Second Floor																							
INT2A.1720	Install Toilets & Urinals, Second Floor Area A Bathrooms	2	11-Sep-23	12-Sep-23	109	■ Install Toilets & Urinals, Second Floor Area A Bathrooms																							
INT2A.3050	Install Partitions, Second Floor Area A Bathrooms	5	13-Sep-23	19-Sep-23	109	■ Install Partitions, Second Floor Area A Bathrooms																							
INT2A.3060	Install Toilet Accessories, Second Floor Area A Bathrooms	2	20-Sep-23	21-Sep-23	109	■ Install Toilet Accessories, Second Floor Area A Bathrooms																							
INT2A.1620	Install Finished Ceilings, Second Floor Area A Bathrooms	2	02-Oct-23	03-Oct-23	88	■ Install Finished Ceilings, Second Floor Area A Bathrooms																							
INT2A.1730	Install Plumbing Fixtures, Second Floor Area A Bathrooms	5	04-Oct-23	10-Oct-23	93	■ Install Plumbing Fixtures, Second Floor Area A Bathrooms																							
INT2A.1710	Install Wall Tile, Second Floor Area A Bathrooms	5	04-Oct-23	10-Oct-23	88	■ Install Wall Tile, Second Floor Area A Bathrooms																							
INT2A.1680	Install Tile Flooring, Second Floor Area A Bathrooms	5	11-Oct-23	17-Oct-23	88	■ Install Tile Flooring, Second Floor Area A Bathrooms																							
INT2A.1670	Apply Finish Paint, Second Floor Area A Bathrooms	2	18-Oct-23	19-Oct-23	88	■ Apply Finish Paint, Second Floor Area A Bathrooms																							
INT2A.1690	Install Interior Signage, Second Floor Area A Bathrooms	1	20-Oct-23	20-Oct-23	88	■ Install Interior Signage, Second Floor Area A Bathrooms																							
INT2A.1700	Final Clean Second Floor Area A Bathrooms	5	11-Mar-24	15-Mar-24	-9	■ Final Clean Second Floor Area A Bathrooms																							
Area A Electrical Room 2106 Second Floor		10	08-Apr-24	19-Apr-24	-14	▼ 19-Apr-24, Area A Electrical Room 2106 Second Floor																							
INT2A.1750	Set Switchgear / Cabling / Terminations, First Floor Electrical Room 2106	5	08-Apr-24	12-Apr-24	-14	■ Set Switchgear / Cabling / Terminations, First Floor Electrical Room 2106																							
INT2A.1760	Install Electrical & Data Devices, First Floor Electrical Room 2106	5	15-Apr-24	19-Apr-24	-14	■ Install Electrical & Data Devices, First Floor Electrical Room 2106																							
Area A - Third Floor		137	11-Sep-23	22-Mar-24	-9	▼ 22-Mar-24, Area A - Third Floor																							
Area A Corridors & BOH - Third Floor		132	18-Sep-23	22-Mar-24	-9	▼ 22-Mar-24, Area A Corridors & BOH - Third Floor																							
INT1A.3100	Install GFCMU Alternate #5, Third Floor Area A	3	20-Sep-23	22-Sep-23	91	■ Install GFCMU Alternate #5, Third Floor Area A																							
Area A Rough-in Corridors & BOH Third Floor		10	18-Sep-23	29-Sep-23	86	▼ 29-Sep-23, Area A Rough-in Corridors & BOH Third Floor																							
INT3A.1420	Apply Prime Paint, Third Floor Area A Corridors & BOH	5	18-Sep-23	22-Sep-23	66	■ Apply Prime Paint, Third Floor Area A Corridors & BOH																							
INT3A.1350	Frame Ceilings, Third Floor Area A Corridors & BOH	5	25-Sep-23	29-Sep-23	86	■ Frame Ceilings, Third Floor Area A Corridors & BOH																							
INT3A.1440	Perform Overhead Inspection, Third Floor Area A Corridors & BOH	0		29-Sep-23	86	◆ Perform Overhead Inspection, Third Floor Area A Corridors & BOH																							
Area A MEP's Corridors & BOH Third Floor		15	25-Sep-23	13-Oct-23	98	▼ 13-Oct-23, Area A MEP's Corridors & BOH Third Floor																							
INT3A.1380	Install Finish Plumbing Drinking Fountains, Third Floor Area A Corridors & BOH	10	25-Sep-23	06-Oct-23	96	■ Install Finish Plumbing Drinking Fountains, Third Floor Area A Corridors & BOH																							
INT3A.1400	Install Sprinkler Heads, Third Floor Area A Corridors & BOH	3	02-Oct-23	04-Oct-23	98	■ Install Sprinkler Heads, Third Floor Area A Corridors & BOH																							
INT3A.1390	Install Lighting, Third Floor Area A Corridors & BOH	5	09-Oct-23	13-Oct-23	98	■ Install Lighting, Third Floor Area A Corridors & BOH																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 23 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area B Bathrooms - Second Floor		163	01-Sep-23 A	22-Apr-24	10	22-Apr-24, Area B Bathrooms - Second Floor																							
Area B Rough-in Bathrooms Second Floor		25	01-Sep-23 A	29-Sep-23	132	29-Sep-23, Area B Rough-in Bathrooms Second Floor																							
INT2B.1590	Install In-Wall Insulation, Second Floor Area B Bathrooms	5	01-Sep-23 A	15-Sep-23	132	Install In-Wall Insulation, Second Floor Area B Bathrooms																							
INT2B.1640	Install Gypsum Wallboard, Second Floor Area B Bathrooms	5	01-Sep-23 A	15-Sep-23	132	Install Gypsum Wallboard, Second Floor Area B Bathrooms																							
INT2B.1680	Apply Prime Paint, Second Floor Area B Bathrooms	5	18-Sep-23	22-Sep-23	132	Apply Prime Paint, Second Floor Area B Bathrooms																							
INT2B.1250	Frame Ceilings, Second Floor Area B Bathrooms	5	25-Sep-23	29-Sep-23	132	Frame Ceilings, Second Floor Area B Bathrooms																							
INT2B.1370	Perform Overhead Inspection, Second Floor Area B Bathrooms	0		29-Sep-23	132	Perform Overhead Inspection, Second Floor Area B Bathrooms																							
Area B MEP's Bathrooms Second Floor		7	02-Oct-23	10-Oct-23	140	10-Oct-23, Area B MEP's Bathrooms Second Floor																							
INT2B.1450	Install Sprinkler Heads, Second Floor Area B Bathrooms	3	02-Oct-23	04-Oct-23	141	Install Sprinkler Heads, Second Floor Area B Bathrooms																							
INT2B.1520	Install Lighting, Second Floor Area B Bathrooms	5	04-Oct-23	10-Oct-23	140	Install Lighting, Second Floor Area B Bathrooms																							
INT2B.1510	Install Mechanical Finishes, Chilled Beams Second Floor Area B Bathrooms	2	04-Oct-23	05-Oct-23	143	Install Mechanical Finishes, Chilled Beams Second Floor Area B Bathrooms																							
Area B Finishes Bathrooms Second Floor		157	11-Sep-23	22-Apr-24	10	22-Apr-24, Area B Finishes Bathrooms Second Floor																							
INT2B.1470	Install Plumbing Fixtures, Second Floor Area B Bathrooms	5	11-Sep-23	15-Sep-23	154	Install Plumbing Fixtures, Second Floor Area B Bathrooms																							
INT2B.1690	Install Toilets & Urinals, Second Floor Area B Bathrooms	2	18-Sep-23	19-Sep-23	148	Install Toilets & Urinals, Second Floor Area B Bathrooms																							
INT2B.2990	Install Partitions, Second Floor Area B Bathrooms	5	20-Sep-23	26-Sep-23	148	Install Partitions, Second Floor Area B Bathrooms																							
INT2B.3000	Install Toilet Accessories, Second Floor Area B Bathrooms	2	27-Sep-23	28-Sep-23	148	Install Toilet Accessories, Second Floor Area B Bathrooms																							
INT2B.1460	Install Finished Ceilings, Second Floor Area B Bathrooms	2	02-Oct-23	03-Oct-23	132	Install Finished Ceilings, Second Floor Area B Bathrooms																							
INT2B.1530	Install Wall Tile, Second Floor Area B Bathrooms	5	04-Oct-23	10-Oct-23	132	Install Wall Tile, Second Floor Area B Bathrooms																							
INT2B.1620	Install Tile Flooring, Second Floor Area B Bathrooms	5	11-Oct-23	17-Oct-23	132	Install Tile Flooring, Second Floor Area B Bathrooms																							
INT2B.1720	Apply Finish Paint, Second Floor Area B Bathrooms	2	18-Oct-23	19-Oct-23	132	Apply Finish Paint, Second Floor Area B Bathrooms																							
INT2B.1730	Install Interior Signage, Second Floor Area B Bathrooms	1	20-Oct-23	20-Oct-23	132	Install Interior Signage, Second Floor Area B Bathrooms																							
INT2B.1740	Final Clean Second Floor Area B Bathrooms	5	16-Apr-24	22-Apr-24	10	Final Clean Second Floor Area B Bathrooms																							
Area B Electrical Room 2106 Second Floor		10	29-Apr-24	10-May-24	-14	10-May-24, Area B Electrical Room 2106 Second Floor																							
INT2B.1320	Set Switchgear / Cabling / Terminations, First Floor Electrical Room 2106	5	29-Apr-24	03-May-24	-14	Set Switchgear / Cabling / Terminations, First Floor Electrical Room 2106																							
INT2B.1480	Install Electrical & Data Devices, First Floor Electrical Room 2106	5	06-May-24	10-May-24	-14	Install Electrical & Data Devices, First Floor Electrical Room 2106																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 24 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area B - Third Floor		185	08-Sep-23 A	24-May-24	199	24-May-24, Area B - Third Floor																							
Area B Corridors & BOH - Third Floor		42	08-Sep-23 A	07-Nov-23	115	07-Nov-23, Area B Corridors & BOH - Third Floor																							
INT3B.3040	Install GFCMU Alternate #5, Third Floor Area B	4	05-Oct-23	10-Oct-23	128	Install GFCMU Alternate #5, Third Floor Area B																							
Area B Rough-in Corridors & BOH Third Floor		26	08-Sep-23 A	29-Sep-23	115	29-Sep-23, Area B Rough-in Corridors & BOH Third Floor																							
INT3B.1160	Install In-Wall Insulation, Third Floor Area B Corridors & BOH	5	08-Sep-23 A	15-Sep-23	115	Install In-Wall Insulation, Third Floor Area B Corridors & BOH																							
INT3B.1230	Install Gypsum Wallboard, Third Floor Area B Corridors & BOH	5	08-Sep-23 A	15-Sep-23	115	Install Gypsum Wallboard, Third Floor Area B Corridors & BOH																							
INT3B.1350	Apply Prime Paint, Third Floor Area B Corridors & BOH	5	18-Sep-23	22-Sep-23	115	Apply Prime Paint, Third Floor Area B Corridors & BOH																							
INT3B.1050	Frame Ceilings, Third Floor Area B Corridors & BOH	5	25-Sep-23	29-Sep-23	115	Frame Ceilings, Third Floor Area B Corridors & BOH																							
INT3B.1270	Perform Overhead Inspection, Third Floor Area B Corridors & BOH	0		29-Sep-23	115	Perform Overhead Inspection, Third Floor Area B Corridors & BOH																							
Area B MEP's Corridors & BOH Third Floor		15	25-Sep-23	13-Oct-23	127	13-Oct-23, Area B MEP's Corridors & BOH Third Floor																							
INT3B.1500	Install Finish Plumbing Drinking Fountains, Third Floor Area B Corridors & BOH	10	25-Sep-23	06-Oct-23	125	Install Finish Plumbing Drinking Fountains, Third Floor Area B Corridors & BOH																							
INT3B.1290	Install Sprinkler Heads, Third Floor Area B Corridors & BOH	3	02-Oct-23	04-Oct-23	127	Install Sprinkler Heads, Third Floor Area B Corridors & BOH																							
INT3B.1410	Install Lighting, Third Floor Area B Corridors & BOH	5	09-Oct-23	13-Oct-23	127	Install Lighting, Third Floor Area B Corridors & BOH																							
INT3B.1400	Install Mechanical Finishes, Chilled Beams Third Floor Area B Corridors & BOH	5	09-Oct-23	13-Oct-23	127	Install Mechanical Finishes, Chilled Beams Third Floor Area B Corridors & BOH																							
Area B Finishes Corridors & BOH Third Floor		42	11-Sep-23	07-Nov-23	115	07-Nov-23, Area B Finishes Corridors & BOH Third Floor																							
INT3B.1800	Install & Start-up RTU 14	10	11-Sep-23	22-Sep-23	142	Install & Start-up RTU 14																							
INT3B.1300	Install Finished Ceilings, Third Floor Area B Corridors & BOH	5	02-Oct-23	06-Oct-23	115	Install Finished Ceilings, Third Floor Area B Corridors & BOH																							
INT3B.1420	Install Finish Flooring, Third Floor Area B Corridors & BOH	10	09-Oct-23	20-Oct-23	115	Install Finish Flooring, Third Floor Area B Corridors & BOH																							
INT3B.1660	Apply Finish Paint, Third Floor Area B Corridors & BOH	5	23-Oct-23	27-Oct-23	115	Apply Finish Paint, Third Floor Area B Corridors & BOH																							
INT3B.1700	Install Interior Signage, Third Floor Area B Corridors & BOH	2	30-Oct-23	31-Oct-23	115	Install Interior Signage, Third Floor Area B Corridors & BOH																							
INT3B.1710	Final Clean Third Floor Area B Corridors & BOH	5	01-Nov-23	07-Nov-23	115	Final Clean Third Floor Area B Corridors & BOH																							
Area B Classrooms & Labs Third Floor		166	08-Sep-23 A	29-Apr-24	0	29-Apr-24, Area B Classrooms & Labs Third Floor																							
Area B Rough-in Classrooms & Labs Third Floor		19	08-Sep-23 A	29-Sep-23	110	29-Sep-23, Area B Rough-in Classrooms & Labs Third Floor																							
INT3B.1220	Install In-Wall Insulation, Third Floor Area B Classrooms	5	08-Sep-23 A	15-Sep-23	110	Install In-Wall Insulation, Third Floor Area B Classrooms																							
INT3B.1340	Install Gypsum Wallboard, Third Floor Area B Classrooms	5	08-Sep-23 A	15-Sep-23	110	Install Gypsum Wallboard, Third Floor Area B Classrooms																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 28 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
INT1C.1460	Apply Finish Paint, First Floor Area C Corridors & BOH	5	20-Nov-23	27-Nov-23	101			■																					
INT1C.1480	Install Interior Signage, First Floor Area C Corridors & BOH	2	28-Nov-23	29-Nov-23	101			■																					
INT1C.1490	Final Clean First Floor Area C Corridors & BOH	5	30-Nov-23	06-Dec-23	101			■																					
Area C Classrooms, Auto Shop & Wood Shop First Floor		175	20-Jul-23 A	13-May-24	1	▶ 13-May-24, Area C Classrooms, Auto Shop & Wood Shop First Floor																							
Area C Rough-in Classrooms, Auto Shop & Wood Shop First Floor		45	20-Jul-23 A	10-Nov-23	106	▶ 10-Nov-23, Area C Rough-in Classrooms, Auto Shop & Wood Shop First Floor																							
INT1C.1050	Install Sprinkler Mains, First Floor Area C Classrooms	5	20-Jul-23 A	11-Sep-23	131	■																							
INT1C.1040	Install VAV's, First Floor Area C Classrooms	5	11-Sep-23	15-Sep-23	131	■																							
INT1C.1180	Install In-Wall Insulation, First Floor Area C Classrooms	5	14-Sep-23	20-Sep-23	118	■																							
INT1C.1160	Perform In-Wall Inspection, First Floor Area C Classrooms	0		20-Sep-23	118	◆																							
INT1C.1070	Frame Ceilings, First Floor Area C Classrooms	5	23-Oct-23	27-Oct-23	101	■																							
INT1C.1170	Perform Overhead Inspection, First Floor Area C Classrooms	0		27-Oct-23	101	◆																							
INT1C.1000	Install Gypsum Wallboard, First Floor Area C Classrooms	5	30-Oct-23	03-Nov-23	91	■																							
INT1C.1150	Apply Prime Paint, First Floor Area C Classrooms	5	06-Nov-23	10-Nov-23	106	■																							
Area C MEP's Classrooms, Auto Shop & Wood Shop First Floor		58	20-Jul-23 A	27-Nov-23	113	▶ 27-Nov-23, Area C MEP's Classrooms, Auto Shop & Wood Shop First Floor																							
INT1C.1080	Install Rough Fire Protection, First Floor Area C Classrooms	3	20-Jul-23 A	13-Sep-23	118	■																							
INT1C.1060	Install Overhead Duct Mains, First Floor Area C Classrooms	10	11-Sep-23	22-Sep-23	121	■																							
INT1C.1030	Install Rough HVAC, First Floor Area C Classrooms	3	11-Sep-23	13-Sep-23	118	■																							
INT1C.1120	Install Sprinkler Heads, First Floor Area C Classrooms	3	30-Oct-23	01-Nov-23	123	■																							
INT1C.1230	Install AV Equipment, First Floor Area C	3	06-Nov-23	08-Nov-23	118	■																							
INT1C.1190	Install Tele / Data Finishes, First Floor Area C Classrooms	5	06-Nov-23	10-Nov-23	116	■																							
INT1C.1110	Install Lighting, First Floor Area C Classrooms	5	06-Nov-23	10-Nov-23	123	■																							
INT1C.1090	Install Mechanical Finishes, Chilled Beams First Floor Area C Classrooms	5	06-Nov-23	10-Nov-23	113	■																							
INT1C.1770	Install Finish Lab Equipment, First Floor Area C Classrooms	10	13-Nov-23	27-Nov-23	113	■																							
INT1C.1100	Install Finish Plumbing, First Floor Area C Classrooms	10	13-Nov-23	27-Nov-23	106	■																							
Area C Finishes Classrooms, Auto Shop & Wood Shop First Floor		172	11-Sep-23	13-May-24	1	▶ 13-May-24, Area C Finishes Classrooms, Auto Shop & Wood Shop First Floor																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 30 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025							
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
INT1C.1600	Install Lighting, First Floor Area C Bathrooms	5	02-Oct-23	06-Oct-23	143																				
INT1C.1590	Install Mechanical Finishes, Chilled Beams First Floor Area C Bathrooms	2	02-Oct-23	03-Oct-23	146																				
Area C Finishes Bathrooms First Floor		59	21-Sep-23	13-Dec-23	101																				
INT1C.1730	Install Plumbing Fixtures, First Floor Area C Bathrooms	5	21-Sep-23	27-Sep-23	147																				
INT1C.1620	Install Finished Ceilings, First Floor Area C Bathrooms	2	28-Sep-23	29-Sep-23	135																				
INT1C.1710	Install Wall Tile, First Floor Area C Bathrooms	5	02-Oct-23	06-Oct-23	135																				
INT1C.1680	Install Tile Flooring, First Floor Area C Bathrooms	5	09-Oct-23	13-Oct-23	135																				
INT1C.1720	Install Toilets & Urinals, First Floor Area C Bathrooms	2	06-Nov-23	07-Nov-23	114																				
INT1C.2970	Install Partitions, First Floor Area C Bathrooms	5	08-Nov-23	14-Nov-23	114																				
INT1C.1670	Apply Finish Paint, First Floor Area C Bathrooms	2	13-Nov-23	14-Nov-23	115																				
INT1C.2980	Install Toilet Accessories, First Floor Area C Bathrooms	2	15-Nov-23	16-Nov-23	114																				
INT1C.1690	Install Interior Signage, First Floor Area C Bathrooms	1	15-Nov-23	15-Nov-23	115																				
INT1C.1700	Final Clean First Floor Area C Bathrooms	5	07-Dec-23	13-Dec-23	101																				
Area C - Second Floor		188	08-Aug-23 A	04-Jun-24	1																				
Area C Corridors & BOH - Second Floor		178	08-Aug-23 A	20-May-24	1																				
INT2C.2990	Install GFCMU Alternate #5, Second Floor Area C	4	17-Oct-23	20-Oct-23	128																				
Area C Rough-in Corridors & BOH Second Floor		49	05-Sep-23 A	17-Nov-23	106																				
INT2C.1180	Install VAV's, Second Floor Area C Corridors & BOH	5	05-Sep-23 A	15-Sep-23	146																				
INT2C.1050	Frame Ceilings, Second Floor Area C Corridors & BOH	5	14-Sep-23	20-Sep-23	143																				
INT2C.1160	Install In-Wall Insulation, Second Floor Area C Corridors & BOH	5	18-Sep-23	22-Sep-23	121																				
INT2C.1260	Perform Overhead Inspection, Second Floor Area C Corridors & BOH	0		20-Sep-23	143																				
INT2C.1210	Perform In-Wall Inspection, Second Floor Area C Corridors & BOH	0		22-Sep-23	121																				
INT2C.1230	Install Gypsum Wallboard, Second Floor Area C Corridors & BOH	5	06-Nov-23	10-Nov-23	91																				
INT2C.1330	Apply Prime Paint, Second Floor Area C Corridors & BOH	5	13-Nov-23	17-Nov-23	106																				
Area C MEP's Corridors & BOH Second Floor		61	08-Aug-23 A	04-Dec-23	113																				



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 31 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025													
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug		
INT2C.1040	Install Rough Plumbing, Second Floor Area C Corridors & BOH	3	08-Aug-23 A	13-Sep-23	121	█																									
INT2C.1080	Install Rough Electrical & Communications, Second Floor Area C Corridors & BOH	5	06-Sep-23 A	15-Sep-23	121	█																									
INT2C.1280	Install Sprinkler Heads, Second Floor Area C Corridors & BOH	3	21-Sep-23	25-Sep-23	155	█																									
INT2C.1390	Install Lighting, Second Floor Area C Corridors & BOH	5	28-Sep-23	04-Oct-23	155	█																									
INT2C.1380	Install Mechanical Finishes, Chilled Beams Second Floor Area C Corridors & BOH	5	28-Sep-23	04-Oct-23	155	█																									
INT2C.1470	Install Finish Plumbing Drinking Fountains, Second Floor Area C Corridors & BOH	10	20-Nov-23	04-Dec-23	106				█																						
Area C Finishes Corridors & BOH Second Floor		169	21-Sep-23	20-May-24	1	▶ 20-May-24, Area C Finishes Corridors & BOH Second Floor																									
INT2C.1290	Install Finished Ceilings, Second Floor Area C Corridors & BOH	5	21-Sep-23	27-Sep-23	143	█																									
INT2C.1400	Install Finish Flooring, Second Floor Area C Corridors & BOH	10	28-Sep-23	11-Oct-23	143	█																									
INT2C.1630	Apply Finish Paint, Second Floor Area C Corridors & BOH	5	05-Dec-23	11-Dec-23	106				█																						
INT2C.1670	Install Interior Signage, Second Floor Area C Corridors & BOH	2	12-Dec-23	13-Dec-23	106				█																						
INT2C.1680	Final Clean Second Floor Area C Corridors & BOH	5	14-May-24	20-May-24	1																					█					
Area C Classrooms & Arts Second Floor		186	08-Aug-23 A	04-Jun-24	1	▶ 04-Jun-24, Area C Classrooms & Arts Second Floor																									
Area C Rough-in Classrooms & Arts Second Floor		54	05-Sep-23 A	27-Nov-23	111	▶ 27-Nov-23, Area C Rough-in Classrooms & Arts Second Floor																									
INT2C.1270	Install VAV's, Second Floor Area C Classrooms	5	05-Sep-23 A	15-Sep-23	141	█																									
INT2C.1110	Frame Ceilings, Second Floor Area C Classrooms	5	14-Sep-23	20-Sep-23	138	█																									
INT2C.1340	Perform Overhead Inspection, Second Floor Area C Classrooms	0		20-Sep-23	138	◆																									
INT2C.1220	Install In-Wall Insulation, Second Floor Area C Classrooms	5	21-Sep-23	27-Sep-23	123	█																									
INT2C.1310	Perform In-Wall Inspection, Second Floor Area C Classrooms	0		27-Sep-23	123	◆																									
INT2C.1320	Install Gypsum Wallboard, Second Floor Area C Classrooms	5	13-Nov-23	17-Nov-23	91				█																						
INT2C.1460	Apply Prime Paint, Second Floor Area C Classrooms	5	20-Nov-23	27-Nov-23	111				█																						
Area C MEP's Classrooms & Arts Second Floor		62	08-Aug-23 A	11-Dec-23	118	▶ 11-Dec-23, Area C MEP's Classrooms & Arts Second Floor																									
INT2C.1100	Install Rough Plumbing, Second Floor Area C Classrooms	3	08-Aug-23 A	13-Sep-23	123	█																									
INT2C.1140	Install Rough Electrical & Communications, Second Floor Area C Classrooms	5	14-Sep-23	20-Sep-23	123	█																									
INT2C.1360	Install Sprinkler Heads, Second Floor Area C Classrooms	3	21-Sep-23	25-Sep-23	165	█																									



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 33 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
INT2C.1410	Install Rough Electrical & Communications, Second Floor Area C Bathrooms	5	21-Sep-23	27-Sep-23	146	■ Install Rough Electrical & Communications, Second Floor Area C Bathrooms																							
INT2C.1430	Install Sprinkler Heads, Second Floor Area C Bathrooms	3	28-Sep-23	02-Oct-23	159	■ Install Sprinkler Heads, Second Floor Area C Bathrooms																							
INT2C.1490	Install Lighting, Second Floor Area C Bathrooms	5	02-Oct-23	06-Oct-23	158	■ Install Lighting, Second Floor Area C Bathrooms																							
INT2C.1480	Install Mechanical Finishes, Chilled Beams Second Floor Area C Bathrooms	2	02-Oct-23	03-Oct-23	161	■ Install Mechanical Finishes, Chilled Beams Second Floor Area C Bathrooms																							
Area C Finishes Bathrooms Second Floor		174	21-Sep-23	28-May-24	1	▶ 28-May-24, Area C Finishes Bathrooms Second Floor																							
INT2C.1450	Install Plumbing Fixtures, Second Floor Area C Bathrooms	5	21-Sep-23	27-Sep-23	162	■ Install Plumbing Fixtures, Second Floor Area C Bathrooms																							
INT2C.1440	Install Finished Ceilings, Second Floor Area C Bathrooms	2	28-Sep-23	29-Sep-23	150	■ Install Finished Ceilings, Second Floor Area C Bathrooms																							
INT2C.1500	Install Wall Tile, Second Floor Area C Bathrooms	5	02-Oct-23	06-Oct-23	150	■ Install Wall Tile, Second Floor Area C Bathrooms																							
INT2C.1590	Install Tile Flooring, Second Floor Area C Bathrooms	5	09-Oct-23	13-Oct-23	150	■ Install Tile Flooring, Second Floor Area C Bathrooms																							
INT2C.1660	Install Toilets & Urinals, Second Floor Area C Bathrooms	2	20-Nov-23	21-Nov-23	119	■ Install Toilets & Urinals, Second Floor Area C Bathrooms																							
INT2C.2950	Install Partitions, Second Floor Area C Bathrooms	5	22-Nov-23	29-Nov-23	119	■ Install Partitions, Second Floor Area C Bathrooms																							
INT2C.1690	Apply Finish Paint, Second Floor Area C Bathrooms	2	28-Nov-23	29-Nov-23	120	■ Apply Finish Paint, Second Floor Area C Bathrooms																							
INT2C.2960	Install Toilet Accessories, Second Floor Area C Bathrooms	2	30-Nov-23	01-Dec-23	119	■ Install Toilet Accessories, Second Floor Area C Bathrooms																							
INT2C.1700	Install Interior Signage, Second Floor Area C Bathrooms	1	30-Nov-23	30-Nov-23	120	■ Install Interior Signage, Second Floor Area C Bathrooms																							
INT2C.1710	Final Clean Second Floor Area C Bathrooms	5	21-May-24	28-May-24	1	■ Final Clean Second Floor Area C Bathrooms																							
VERTICAL TRANSPORTATION Area C		22	03-Nov-23	05-Dec-23	117	▶ 05-Dec-23, VERTICAL TRANSPORTATION Area C																							
Area C STAIRS 4 S4		22	03-Nov-23	05-Dec-23	117	▶ 05-Dec-23, Area C STAIRS 4 S4																							
INT2C.1750	Erect Stair 3	10	03-Nov-23	16-Nov-23	117	■ Erect Stair 3																							
INT2C.2970	Erect Stair 4	10	17-Nov-23	01-Dec-23	117	■ Erect Stair 4																							
INT2C.1760	Pour Stair Treads S3	2	17-Nov-23	20-Nov-23	127	■ Pour Stair Treads S3																							
INT2C.2980	Pour Stair Treads S4	2	04-Dec-23	05-Dec-23	117	■ Pour Stair Treads S4																							
AREA D INTERIORS GYMNASIUMS, LOCKER / WEIGHT RMs, K		216	30-Aug-23 A	10-Jul-24	1	▶ 10-Jul-24, AREA D INTERIORS GYMNASIUMS, LOCKER / WEIGHT RMs, KITCHEN, S																							
Area D - First Floor		201	30-Aug-23 A	24-Jun-24	12	▶ 24-Jun-24, Area D - First Floor																							
INT1D.1330	Layout & Frame CMU Walls, First Floor Area D	15	01-Sep-23 A	29-Sep-23	27	■ Layout & Frame CMU Walls, First Floor Area D																							
INT1D.2540	Install GFCMU Alternate #5, First Floor Area D	9	23-Oct-23	02-Nov-23	128	■ Install GFCMU Alternate #5, First Floor Area D																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area D LG Gym 1452 First Floor		150	11-Sep-23	11-Apr-24	58	11-Apr-24, Area D LG Gym 1452 First Floor																							
Area D Rough-in LG Gym 1452 First Floor		52	25-Sep-23	06-Dec-23	123	06-Dec-23, Area D Rough-in LG Gym 1452 First Floor																							
INT1D.2880	Install Sprinkler Mains, First Floor Area D LG Gym	5	25-Sep-23	29-Sep-23	165	Install Sprinkler Mains, First Floor Area D LG Gym																							
INT1D.2870	Install VAV's, First Floor Area D LG Gym	5	02-Oct-23	06-Oct-23	165	Install VAV's, First Floor Area D LG Gym																							
INT1D.3010	Perform Overhead Inspection, First Floor Area D LG Gym	0		06-Oct-23	165	Perform Overhead Inspection, First Floor Area D LG Gym																							
INT1D.3020	Install In-Wall Insulation, First Floor Area D LG Gym	5	22-Nov-23	29-Nov-23	49	Install In-Wall Insulation, First Floor Area D LG Gym																							
INT1D.3000	Perform In-Wall Inspection, First Floor Area D LG Gym	0		29-Nov-23	49	Perform In-Wall Inspection, First Floor Area D LG Gym																							
INT1D.2990	Apply Prime Paint, First Floor Area D LG Gym	5	30-Nov-23	06-Dec-23	49	Apply Prime Paint, First Floor Area D LG Gym																							
Area D MEP's LG Gym 1452 First Floor		77	11-Sep-23	28-Dec-23	126	28-Dec-23, Area D MEP's LG Gym 1452 First Floor																							
INT1D.2890	Install Overhead Duct Mains, First Floor Area D LG Gym	10	11-Sep-23	22-Sep-23	68	Install Overhead Duct Mains, First Floor Area D LG Gym																							
INT1D.2860	Install Rough HVAC, First Floor Area D LG Gym	3	25-Sep-23	27-Sep-23	68	Install Rough HVAC, First Floor Area D LG Gym																							
INT1D.2850	Install Rough Plumbing, First Floor Area D LG Gym	10	28-Sep-23	11-Oct-23	68	Install Rough Plumbing, First Floor Area D LG Gym																							
INT1D.2970	Install Sprinkler Heads, First Floor Area D LG Gym	3	09-Oct-23	11-Oct-23	165	Install Sprinkler Heads, First Floor Area D LG Gym																							
INT1D.2930	Install Rough Fire Protection, First Floor Area D LG Gym	10	12-Oct-23	25-Oct-23	68	Install Rough Fire Protection, First Floor Area D LG Gym																							
INT1D.2840	Install Rough Electrical & Communications, First Floor Area D LG Gym	10	12-Oct-23	25-Oct-23	68	Install Rough Electrical & Communications, First Floor Area D LG Gym																							
INT1D.2960	Install Gym Lighting, First Floor Area D LG Gym	10	07-Dec-23	20-Dec-23	49	Install Gym Lighting, First Floor Area D LG Gym																							
INT1D.2940	Install Mechanical Finishes, Chilled Beams First Floor Area D LG Gym	5	07-Dec-23	13-Dec-23	126	Install Mechanical Finishes, Chilled Beams First Floor Area D LG Gym																							
INT1D.2950	Install Finish Plumbing Drinking Fountains, First Floor Area D LG Gym	10	14-Dec-23	28-Dec-23	126	Install Finish Plumbing Drinking Fountains, First Floor Area D LG Gym																							
INT1D.3310	Install Sound System Finishes, Area D LG Gym First Floor	5	21-Dec-23	28-Dec-23	49	Install Sound System Finishes, Area D LG Gym First Floor																							
Area D Finishes LG Gym 1452 First Floor		150	11-Sep-23	11-Apr-24	58	11-Apr-24, Area D Finishes LG Gym 1452 First Floor																							
INT1D.3400	Install Wall Pads, Area D LG Gym First Floor	5	11-Sep-23	15-Sep-23	183	Install Wall Pads, Area D LG Gym First Floor																							
INT1D.3740	Install & Start-up RTU 01	10	28-Nov-23	11-Dec-23	91	Install & Start-up RTU 01																							
INT1D.3320	Install Doors & Hardware, Area D LG Gym First Floor	10	29-Dec-23	12-Jan-24	49	Install Doors & Hardware, Area D LG Gym First Floor																							
INT1D.3330	Install Gym Equipment, Area D LG Gym First Floor	15	15-Jan-24	02-Feb-24	49	Install Gym Equipment, Area D LG Gym First Floor																							
INT1D.3340	Install Scoreboards, Area D LG Gym First Floor	5	05-Feb-24	09-Feb-24	49	Install Scoreboards, Area D LG Gym First Floor																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 44 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
INT2D.1330	Perform In-Wall Inspection, Second Floor Area D Classrooms	0		02-Oct-23	152	◆ Perform In-Wall Inspection, Second Floor Area D Classrooms																							
INT2D.1360	Perform Overhead Inspection, Second Floor Area D Classrooms	0		04-Oct-23	153	◆ Perform Overhead Inspection, Second Floor Area D Classrooms																							
INT2D.1340	Install Gypsum Wallboard, Second Floor Area D Classrooms	5	11-Jan-24	17-Jan-24	83	■ Install Gypsum Wallboard, Second Floor Area D Classrooms																							
INT2D.1450	Apply Prime Paint, Second Floor Area D Classrooms	5	18-Jan-24	24-Jan-24	91	■ Apply Prime Paint, Second Floor Area D Classrooms																							
Area D MEP's Classrooms & Specialty Rooms Second Floor		99	01-Sep-23 A	07-Feb-24	98	→ 07-Feb-24, Area D MEP's Classrooms & Specialty Rooms Second Floor																							
INT2D.1090	Install Overhead Duct Mains, Second Floor Area D Classrooms	10	01-Sep-23 A	27-Sep-23	153	■ Install Overhead Duct Mains, Second Floor Area D Classrooms																							
INT2D.1080	Install Rough HVAC, Second Floor Area D Classrooms	3	01-Sep-23 A	18-Sep-23	152	■ Install Rough HVAC, Second Floor Area D Classrooms																							
INT2D.1160	Install Rough Fire Protection, Second Floor Area D Classrooms	3	05-Sep-23 A	18-Sep-23	157	■ Install Rough Fire Protection, Second Floor Area D Classrooms																							
INT2D.1120	Install Rough Plumbing, Second Floor Area D Classrooms	3	05-Sep-23 A	18-Sep-23	152	■ Install Rough Plumbing, Second Floor Area D Classrooms																							
INT2D.1150	Install Rough Electrical & Communications, Second Floor Area D Classrooms	5	19-Sep-23	25-Sep-23	152	■ Install Rough Electrical & Communications, Second Floor Area D Classrooms																							
INT2D.1370	Install Sprinkler Heads, Second Floor Area D Classrooms	3	05-Oct-23	09-Oct-23	175	■ Install Sprinkler Heads, Second Floor Area D Classrooms																							
INT2D.1490	Install Lighting, Second Floor Area D Classrooms	5	12-Oct-23	18-Oct-23	175	■ Install Lighting, Second Floor Area D Classrooms																							
INT2D.1480	Install Mechanical Finishes, Chilled Beams Second Floor Area D Classrooms	5	12-Oct-23	18-Oct-23	165	■ Install Mechanical Finishes, Chilled Beams Second Floor Area D Classrooms																							
INT2D.1630	Install Finish Lab Equipment, Second Floor Area D Classrooms	10	19-Oct-23	01-Nov-23	165	■ Install Finish Lab Equipment, Second Floor Area D Classrooms																							
INT2D.1510	Install AV Equipment, Second Floor Area D	3	18-Jan-24	22-Jan-24	103	■ Install AV Equipment, Second Floor Area D																							
INT2D.1500	Install Tele / Data Finishes, Second Floor Area D Classrooms	5	18-Jan-24	24-Jan-24	101	■ Install Tele / Data Finishes, Second Floor Area D Classrooms																							
INT2D.1530	Install Finish Plumbing, Second Floor Area D Classrooms	10	25-Jan-24	07-Feb-24	91	■ Install Finish Plumbing, Second Floor Area D Classrooms																							
Area D Finishes Classrooms & Specialty Rooms Second Floor		189	05-Oct-23	02-Jul-24	1	→ 02-Jul-24, Area D Finishes Classrooms & Specialty Rooms Second Floor																							
INT2D.1380	Install Finished Ceilings, Second Floor Area D Classrooms	5	05-Oct-23	11-Oct-23	153	■ Install Finished Ceilings, Second Floor Area D Classrooms																							
INT2D.1540	Install Visual Display Surfaces, Second Floor Area D Classrooms	3	25-Jan-24	29-Jan-24	105	■ Install Visual Display Surfaces, Second Floor Area D Classrooms																							
INT2D.1740	Install Classroom Casework, First Floor Area D Classrooms	10	17-May-24	31-May-24	1	■ Install Classroom Casework, First Floor Area D Classrooms																							
INT2D.1750	Install Finish Flooring, Second Floor Area D Classrooms	10	03-Jun-24	14-Jun-24	1	■ Install Finish Flooring, Second Floor Area D Classrooms																							
INT2D.1760	Apply Finish Paint, Second Floor Area D Classrooms	5	17-Jun-24	21-Jun-24	1	■ Apply Finish Paint, Second Floor Area D Classrooms																							
INT2D.1770	Install Interior Signage, Second Floor Area D Classrooms	2	24-Jun-24	25-Jun-24	1	■ Install Interior Signage, Second Floor Area D Classrooms																							
INT2D.1780	Final Clean Second Floor Area D Classrooms	5	26-Jun-24	02-Jul-24	1	■ Final Clean Second Floor Area D Classrooms																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 45 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area D Bathrooms - Second Floor		207	01-Sep-23 A	10-Jul-24	1	10-Jul-24, Area D Bathrooms - Second Floor																							
Area D Rough-in Bathrooms Second Floor		95	05-Sep-23 A	31-Jan-24	105	31-Jan-24, Area D Rough-in Bathrooms Second Floor																							
INT2D.1220	Install Sprinkler Mains, Second Floor Area D Bathrooms	5	05-Sep-23 A	15-Sep-23	183	Install Sprinkler Mains, Second Floor Area D Bathrooms																							
INT2D.1320	Install VAV's, Second Floor Area D Bathrooms	5	18-Sep-23	22-Sep-23	183	Install VAV's, Second Floor Area D Bathrooms																							
INT2D.1470	Frame Ceilings, Second Floor Area D Bathrooms	5	21-Sep-23	27-Sep-23	180	Frame Ceilings, Second Floor Area D Bathrooms																							
INT2D.1550	Perform Overhead Inspection, Second Floor Area D Bathrooms	0		27-Sep-23	180	Perform Overhead Inspection, Second Floor Area D Bathrooms																							
INT2D.1520	Install In-Wall Insulation, Second Floor Area D Bathrooms	5	28-Sep-23	04-Oct-23	155	Install In-Wall Insulation, Second Floor Area D Bathrooms																							
INT2D.1580	Perform In-Wall Inspection, Second Floor Area D Bathrooms	0		04-Oct-23	155	Perform In-Wall Inspection, Second Floor Area D Bathrooms																							
INT2D.1590	Install Gypsum Wallboard, Second Floor Area D Bathrooms	5	18-Jan-24	24-Jan-24	83	Install Gypsum Wallboard, Second Floor Area D Bathrooms																							
INT2D.1650	Apply Prime Paint, Second Floor Area D Bathrooms	5	25-Jan-24	31-Jan-24	105	Apply Prime Paint, Second Floor Area D Bathrooms																							
Area D MEP's Bathrooms Second Floor		46	01-Sep-23 A	06-Oct-23	188	06-Oct-23, Area D MEP's Bathrooms Second Floor																							
INT2D.1140	Install Overhead Duct Mains, Second Floor Area D Bathrooms	5	01-Sep-23 A	15-Sep-23	155	Install Overhead Duct Mains, Second Floor Area D Bathrooms																							
INT2D.1210	Install Rough HVAC, Second Floor Area D Bathrooms	2	01-Sep-23 A	12-Sep-23	155	Install Rough HVAC, Second Floor Area D Bathrooms																							
INT2D.1430	Install Rough Fire Protection, Second Floor Area D Bathrooms	3	05-Sep-23 A	13-Sep-23	165	Install Rough Fire Protection, Second Floor Area D Bathrooms																							
INT2D.1260	Install Rough Plumbing, Second Floor Area D Bathrooms	8	05-Sep-23 A	20-Sep-23	155	Install Rough Plumbing, Second Floor Area D Bathrooms																							
INT2D.1420	Install Rough Electrical & Communications, Second Floor Area D Bathrooms	5	21-Sep-23	27-Sep-23	155	Install Rough Electrical & Communications, Second Floor Area D Bathrooms																							
INT2D.1560	Install Sprinkler Heads, Second Floor Area D Bathrooms	3	28-Sep-23	02-Oct-23	189	Install Sprinkler Heads, Second Floor Area D Bathrooms																							
INT2D.1610	Install Lighting, Second Floor Area D Bathrooms	5	02-Oct-23	06-Oct-23	188	Install Lighting, Second Floor Area D Bathrooms																							
INT2D.1600	Install Mechanical Finishes, Chilled Beams Second Floor Area D Bathrooms	2	02-Oct-23	03-Oct-23	191	Install Mechanical Finishes, Chilled Beams Second Floor Area D Bathrooms																							
Area D Finishes Bathrooms Second Floor		204	21-Sep-23	10-Jul-24	1	10-Jul-24, Area D Finishes Bathrooms Second Floor																							
INT2D.1440	Install Plumbing Fixtures, Second Floor Area D Bathrooms	5	21-Sep-23	27-Sep-23	192	Install Plumbing Fixtures, Second Floor Area D Bathrooms																							
INT2D.1570	Install Finished Ceilings, Second Floor Area D Bathrooms	2	28-Sep-23	29-Sep-23	180	Install Finished Ceilings, Second Floor Area D Bathrooms																							
INT2D.1620	Install Wall Tile, Second Floor Area D Bathrooms	5	02-Oct-23	06-Oct-23	180	Install Wall Tile, Second Floor Area D Bathrooms																							
INT2D.1660	Install Tile Flooring, Second Floor Area D Bathrooms	5	09-Oct-23	13-Oct-23	180	Install Tile Flooring, Second Floor Area D Bathrooms																							
INT2D.1670	Install Toilets & Urinals, Second Floor Area D Bathrooms	2	25-Jan-24	26-Jan-24	104	Install Toilets & Urinals, Second Floor Area D Bathrooms																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 49 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area E Auditorium & Stage First Floor		218	06-Sep-23 A	25-Jul-24	180	25-Jul-24, Area E Auditorium & Stage First Floor																							
Area E Rough-in Auditorium & Stage First Floor		152	06-Sep-23 A	22-Apr-24	233	22-Apr-24, Area E Rough-in Auditorium & Stage First Floor																							
INT1E.2890	Install CMU Walls, Area E Auditorium	15	06-Sep-23 A	04-Oct-23	3	Install CMU Walls, Area E Auditorium																							
Area E Upper Works Rough		24	05-Oct-23	07-Nov-23	348	07-Nov-23, Area E Upper Works Rough																							
INT1E.2740	Install Work Platform Upper Works, First Floor Area E Auditorium	5	05-Oct-23	11-Oct-23	3	Install Work Platform Upper Works, First Floor Area E Auditorium																							
INT1E.2750	Install CFMF Perimeter Walls & High Drywall, First Floor Area E Auditorium	10	12-Oct-23	25-Oct-23	357	Install CFMF Perimeter Walls & High Drywall, First Floor Area E Auditorium																							
INT1E.2900	Apply Paint Upper Works, First Floor Area E	2	06-Nov-23	07-Nov-23	31	Apply Paint Upper Works, First Floor Area E																							
Area E Mid Level Works Rough		23	18-Jan-24	19-Feb-24	3	19-Feb-24, Area E Mid Level Works Rough																							
INT1E.2770	Install Lower Works Platform Mid Elevation, First Floor Area E Auditorium	3	18-Jan-24	22-Jan-24	3	Install Lower Works Platform Mid Elevation, First Floor Area E Auditorium																							
INT1E.2780	Install Drywall Perimeter Flanking Walls, First Floor Area E	10	30-Jan-24	12-Feb-24	3	Install Drywall Perimeter Flanking Walls, First Floor Area E																							
INT1E.2790	Apply Paint Mid Elevation Walls, First Floor Area E Auditorium	5	13-Feb-24	19-Feb-24	3	Apply Paint Mid Elevation Walls, First Floor Area E Auditorium																							
Area E Ground Level Works Rough		29	12-Mar-24	22-Apr-24	3	22-Apr-24, Area E Ground Level Works Rough																							
INT1E.2800	Remove Work Platform, First Floor Area E Auditorium	4	12-Mar-24	15-Mar-24	3	Remove Work Platform, First Floor Area E Auditorium																							
INT1E.2810	Install CFMF Lower Level, First Floor Area E	10	18-Mar-24	01-Apr-24	3	Install CFMF Lower Level, First Floor Area E																							
INT1E.1160	Install Drywall Perimeter Flanking & Remaining Walls, First Floor Area E Auditorium	5	09-Apr-24	15-Apr-24	3	Install Drywall Perimeter Flanking & Remaining Walls, First Floor Area E Auditorium																							
INT1E.1170	Apply Paint Low Elevation Walls, First Floor Area E Auditorium	5	16-Apr-24	22-Apr-24	3	Apply Paint Low Elevation Walls, First Floor Area E Auditorium																							
Area E MEP's Auditorium & Stage First Floor		124	12-Oct-23	08-Apr-24	246	08-Apr-24, Area E MEP's Auditorium & Stage First Floor																							
Area E Upper Works MEP's		65	12-Oct-23	15-Jan-24	305	15-Jan-24, Area E Upper Works MEP's																							
INT1E.1030	Install Rough HVAC Upper Works, First Floor Area E Classrooms	10	12-Oct-23	25-Oct-23	3	Install Rough HVAC Upper Works, First Floor Area E Classrooms																							
INT1E.1060	Install Overhead Duct Mains Upper Works, First Floor Area E Classrooms	10	23-Oct-23	03-Nov-23	3	Install Overhead Duct Mains Upper Works, First Floor Area E Classrooms																							
INT1E.1020	Install Rough Plumbing Upper Works, First Floor Area E Classrooms	10	06-Nov-23	17-Nov-23	3	Install Rough Plumbing Upper Works, First Floor Area E Classrooms																							
INT1E.1080	Install Rough Fire Protection Upper Works, First Floor Area E Classrooms	10	20-Nov-23	04-Dec-23	330	Install Rough Fire Protection Upper Works, First Floor Area E Classrooms																							
INT1E.1010	Install Rough Electrical & AV Upper Works, First Floor Area E Classrooms	15	20-Nov-23	11-Dec-23	3	Install Rough Electrical & AV Upper Works, First Floor Area E Classrooms																							
INT1E.2760	Install Wiring & Lighting in Clouds, First Floor Area E Auditorium	5	04-Jan-24	10-Jan-24	3	Install Wiring & Lighting in Clouds, First Floor Area E Auditorium																							
INT1E.1120	Install Fire Protection Drops in Clouds, First Floor Area E Classrooms	3	11-Jan-24	15-Jan-24	305	Install Fire Protection Drops in Clouds, First Floor Area E Classrooms																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 50 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Area E Mid Level Works MEP's						29-Jan-24, Area E Mid Level Works MEP's																							
INT1E.1130	Install Electrical Rough Mid Span Walls, First Floor Area E Auditorium	5	23-Jan-24	29-Jan-24	3	■ Install Electrical Rough Mid Span Walls, First Floor Area E Auditorium																							
Area E Ground Level Works MEP's						08-Apr-24, Area E Ground Level Works MEP's																							
INT1E.1150	Install In-wall Rough Electrical, First Floor Area E Auditorium	5	02-Apr-24	08-Apr-24	3	■ Install In-wall Rough Electrical, First Floor Area E Auditorium																							
Area E Finishes Auditorium & Stage First Floor						25-Jun-24, Area E Finishes Auditorium & Stage First Floor																							
Area E Upper Works Finishes						17-Jan-24, Area E Upper Works Finishes																							
INT1E.1790	Install Millwork Upper Works, Area E Auditorium	32	20-Nov-23	05-Jan-24	6	■ Install Millwork Upper Works, Area E Auditorium																							
INT1E.1800	Install Metal Ceilings, Area E Auditorium	15	28-Nov-23	18-Dec-23	18	■ Install Metal Ceilings, Area E Auditorium																							
INT1E.1140	Install Acoustical Clouds Upper Works, First Floor Area E Auditorium	15	12-Dec-23	03-Jan-24	3	■ Install Acoustical Clouds Upper Works, First Floor Area E Auditorium																							
INT1E.1190	Perform Final Cleaning Upper Works, First Floor Area E Auditorium	5	11-Jan-24	17-Jan-24	3	■ Perform Final Cleaning Upper Works, First Floor Area E Auditorium																							
Area E Mid Level Works Finishes						11-Mar-24, Area E Mid Level Works Finishes																							
INT1E.1210	Install Acoustical Wall Panels Mid Areas, First Floor Area E Auditorium	10	20-Feb-24	04-Mar-24	3	■ Install Acoustical Wall Panels Mid Areas, First Floor Area E Auditorium																							
INT1E.1230	Install Wall Sconces / AV Devices, First Floor Area E Auditorium	5	05-Mar-24	11-Mar-24	3	■ Install Wall Sconces / AV Devices, First Floor Area E Auditorium																							
Area E Ground Level Works Finishes						25-Jun-24, Area E Ground Level Works Finishes																							
INT1E.1750	Install & Start-up RTU 05	10	28-Nov-23	11-Dec-23	105	■ Install & Start-up RTU 05																							
INT1E.1180	Install Acoustical Wall Panels Mid Areas, First Floor Area E Auditorium	10	23-Apr-24	06-May-24	3	■ Install Acoustical Wall Panels Mid Areas, First Floor Area E Auditorium																							
INT1E.2820	Install Acoustical Wall Panels Lower Areas, First Floor Area E Auditorium	10	07-May-24	20-May-24	226	■ Install Acoustical Wall Panels Lower Areas, First Floor Area E Auditorium																							
INT1E.1200	Install Millwork Panels at Front of Stage, First Floor Area E Auditorium	10	07-May-24	20-May-24	3	■ Install Millwork Panels at Front of Stage, First Floor Area E Auditorium																							
INT1E.1220	Apply Epoxy Paint at Seating, First Floor Area E Auditorium	5	21-May-24	28-May-24	3	■ Apply Epoxy Paint at Seating, First Floor Area E Auditorium																							
INT1E.1780	Install Stage Flooring, First Floor Area E Auditorium	10	21-May-24	04-Jun-24	13	■ Install Stage Flooring, First Floor Area E Auditorium																							
INT1E.1240	Install Theatrical Seating, First Floor Area E Auditorium	10	29-May-24	11-Jun-24	3	■ Install Theatrical Seating, First Floor Area E Auditorium																							
INT1E.1250	Install Carpeting & Base, First Floor Area E Auditorium	5	12-Jun-24	18-Jun-24	3	■ Install Carpeting & Base, First Floor Area E Auditorium																							
INT1E.1740	Install Theatrical Lighting, First Floor Area E Auditorium	5	19-Jun-24	25-Jun-24	3	■ Install Theatrical Lighting, First Floor Area E Auditorium																							
Area E Stage Finishes						25-Jul-24, Area E Stage Finishes																							
INT1E.2830	Install Theatrical Lighting, First Floor Area E Stage	6	26-Jun-24	03-Jul-24	3	■ Install Theatrical Lighting, First Floor Area E Stage																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 52 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
INT1E.1620	Install Finished Ceilings, First Floor Area E Bathrooms	2	01-Dec-23	04-Dec-23	138				█																				
INT1E.1710	Install Wall Tile, First Floor Area E Bathrooms	5	05-Dec-23	11-Dec-23	138				█																				
INT1E.1680	Install Tile Flooring, First Floor Area E Bathrooms	5	12-Dec-23	18-Dec-23	138				█																				
INT1E.1720	Install Toilets & Urinals, First Floor Area E Bathrooms	2	08-Feb-24	09-Feb-24	97																								
INT1E.2910	Install Partitions, First Floor Area E Bathrooms	5	12-Feb-24	16-Feb-24	97																								
INT1E.1670	Apply Finish Paint, First Floor Area E Bathrooms	2	15-Feb-24	16-Feb-24	98																								
INT1E.2920	Install Toilet Accessories, First Floor Area E Bathrooms	2	19-Feb-24	20-Feb-24	97																								
INT1E.1690	Install Interior Signage, First Floor Area E Bathrooms	1	19-Feb-24	19-Feb-24	98																								
INT1E.1700	Final Clean First Floor Area E Bathrooms	5	21-Feb-24	27-Feb-24	97																								
Area E - Second Floor		207	25-Sep-23	17-Jul-24	9	▶ 17-Jul-24, Area E - Second Floor																							
Area E Corridors, Concourse, Concourse & BOH - Second Floor		127	25-Sep-23	22-Mar-24	84	▶ 22-Mar-24, Area E Corridors, Concourse, Concourse & BOH - Second Floor																							
INT2E.1000	Install MEP Risers, Second Floor Area E	10	25-Sep-23	06-Oct-23	144				█																				
INT2E.1040	Layout & Frame Interior Walls & Blocking, Second Floor Area E	10	09-Oct-23	20-Oct-23	139				█																				
INT2E.1030	Install GFCMU Alternate #5, Second Floor Area E	3	21-Nov-23	24-Nov-23	140				█																				
Area E Rough-in Corridors, Concourse & BOH Second Floor		80	30-Oct-23	21-Feb-24	84	▶ 21-Feb-24, Area E Rough-in Corridors, Concourse & BOH Second Floor																							
INT2E.1070	Install Sprinkler Mains, Second Floor Area E Corridors & BOH	5	30-Oct-23	03-Nov-23	149				█																				
INT2E.1120	Install VAV's, Second Floor Area E Corridors & BOH	5	06-Nov-23	10-Nov-23	149				█																				
INT2E.1280	Install In-Wall Insulation, Second Floor Area E Corridors & BOH	5	21-Nov-23	28-Nov-23	133				█																				
INT2E.1270	Frame Ceilings, Second Floor Area E Corridors & BOH	5	21-Nov-23	28-Nov-23	138				█																				
INT2E.1410	Perform Overhead Inspection, Second Floor Area E Corridors & BOH	0		28-Nov-23	138				◆																				
INT2E.1400	Perform In-Wall Inspection, Second Floor Area E Corridors & BOH	0		28-Nov-23	133				◆																				
INT2E.1420	Install Gypsum Wallboard, Second Floor Area E Corridors & BOH	5	08-Feb-24	14-Feb-24	84																								
INT2E.1530	Apply Prime Paint, Second Floor Area E Corridors & BOH	5	15-Feb-24	21-Feb-24	84																								
Area E MEP's Corridors, Concourse & BOH Second Floor		100	16-Oct-23	06-Mar-24	91	▶ 06-Mar-24, Area E MEP's Corridors, Concourse & BOH Second Floor																							
INT2E.1050	Install Overhead Duct Mains, Second Floor Area E Corridors & BOH	10	16-Oct-23	27-Oct-23	149				█																				



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 56 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
VERTICAL TRANSPORTATION Area E		55	29-Sep-23	15-Dec-23	371	15-Dec-23, VERTICAL TRANSPORTATION Area E																							
Area E STAIRS 6 S6		10	04-Dec-23	15-Dec-23	371	15-Dec-23, Area E STAIRS 6 S6																							
INT2E.1010	Install Stair 6	5	04-Dec-23	08-Dec-23	371	Install Stair 6																							
INT2E.1020	Pour Stair Treads Stair 6	5	11-Dec-23	15-Dec-23	371	Pour Stair Treads Stair 6																							
Area E ELEVATOR 3 E3		50	29-Sep-23	08-Dec-23	157	08-Dec-23, Area E ELEVATOR 3 E3																							
ELEVE.1000	Install Elevator Shaft E2, Area E	15	29-Sep-23	19-Oct-23	144	Install Elevator Shaft E2, Area E																							
ELEVE.1010	Install Elevator E2, Area E	30	20-Oct-23	01-Dec-23	144	Install Elevator E2, Area E																							
ELEVE.1020	Perform Elevator Inspection E2, Area E	5	04-Dec-23	08-Dec-23	157	Perform Elevator Inspection E2, Area E																							
PHASE 2 NEW HIGH SCHOOL SITEWORK FINISHES		356	07-Dec-23	01-May-25	0	01-May-25, PHASE 2 NEW HIGH SCHOOL SITEWORK FINISHES																							
L1.41 SITEWORK FINISHES		153	07-Dec-23	15-Jul-24	203	15-Jul-24, L1.41 SITEWORK FINISHES																							
L1.41 HARDSCAPES & LANDSCAPES		153	07-Dec-23	15-Jul-24	193	15-Jul-24, L1.41 HARDSCAPES & LANDSCAPES																							
SITEP2.1120	Install Sidewalks, Phase 2 L1.41	10	07-Dec-23	20-Dec-23	277	Install Sidewalks, Phase 2 L1.41																							
SITEP2.1110	Install Hardscapes, Phase 2 L1.41	10	21-Dec-23	05-Jan-24	277	Install Hardscapes, Phase 2 L1.41																							
SITEP2.1130	Perform Landscaping, Phase 2 L1.41	12	17-Jun-24	02-Jul-24	179	Perform Landscaping, Phase 2 L1.41																							
SITEP2.1180	Install Site Furnishes, Phase 2 L1.41	8	03-Jul-24	15-Jul-24	193	Install Site Furnishes, Phase 2 L1.41																							
L1.41 COURTYARDS		15	08-Jan-24	26-Jan-24	277	26-Jan-24, L1.41 COURTYARDS																							
SITEP2.1140	Build Out Courtyards, Phase 2 L1.41	15	08-Jan-24	26-Jan-24	277	Build Out Courtyards, Phase 2 L1.41																							
L1.41 PAVING		24	03-Jun-24	05-Jul-24	209	05-Jul-24, L1.41 PAVING																							
SITEP2.1150	Install Binder, Phase 2 L1.41	10	03-Jun-24*	14-Jun-24	179	Install Binder, Phase 2 L1.41																							
SITEP2.1160	Install Topcourse Paving, Phase 2 L1.41	10	17-Jun-24	28-Jun-24	209	Install Topcourse Paving, Phase 2 L1.41																							
SITEP2.1170	Linestripe, Markings and Install Site Signage, Phase 2 L1.41	4	01-Jul-24	05-Jul-24	209	Linestripe, Markings and Install Site Signage, Phase 2 L1.41																							
L1.42 SITEWORK FINISHES		157	07-Dec-23	19-Jul-24	199	19-Jul-24, L1.42 SITEWORK FINISHES																							
L1.42 HARDSCAPES & LANDSCAPES		157	07-Dec-23	19-Jul-24	179	19-Jul-24, L1.42 HARDSCAPES & LANDSCAPES																							
SITEP2.1220	Perform Site Demolition & Clearing, Phase 2 L1.42	8	07-Dec-23	18-Dec-23	298	Perform Site Demolition & Clearing, Phase 2 L1.42																							
SITEP2.1210	Perform Landscaping, Phase 2 L1.42	12	03-Jul-24	19-Jul-24	179	Perform Landscaping, Phase 2 L1.42																							



O & G Industries, Inc.
Farmington High School and Central Office Projects
- Monthly Update 09 September 2023

Page: 57 of: 60
 Current Date: 14-Sep-23
 BL / UP: 09

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2024												2025											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
L1.42 PAVING						18-Jun-24, L1.42 PAVING																							
SITEP2.1270	Buildout Subgrade Monteith Drive & Parking Lots, Phase 2 L1.42	12	19-Dec-23	05-Jan-24	298	Buildout Subgrade Monteith Drive & Parking Lots, Phase 2 L1.42																							
SITEP2.1260	Install Curbing Monteith Drive & Parking Lots, Phase 2 L1.42	8	27-Dec-23	08-Jan-24	298	Install Curbing Monteith Drive & Parking Lots, Phase 2 L1.42																							
SITEP2.1230	Install Binder Monteith Drive & Parking Lots, Phase 2 L1.42	8	04-Jan-24	15-Jan-24	298	Install Binder Monteith Drive & Parking Lots, Phase 2 L1.42																							
SITEP2.1240	Install Topcourse Paving Monteith Drive & Parking Lots, Phase 2 L1.42	8	03-Jun-24*	12-Jun-24	221	Install Topcourse Paving Monteith Drive & Parking Lots, Phase 2 L1.42																							
SITEP2.1250	Linestripe, Markings and Install Site Signage Monteith Drive & Parking Lots, Phase 2 L1.42	4	13-Jun-24	18-Jun-24	221	Linestripe, Markings and Install Site Signage Monteith Drive & Parking Lots, Phase 2 L1.42																							
L1.43 SITEWORK FINISHES						25-Apr-25, L1.43 SITEWORK FINISHES																							
L1.43 HARDSCAPES & LANDSCAPES						16-Apr-25, L1.43 HARDSCAPES & LANDSCAPES																							
SITEP2.1350	Buildout Grass Field, Phase 2 L1.43	12	01-Apr-25*	16-Apr-25	2	Buildout Grass Field, Phase 2 L1.43																							
SITEP2.1300	Perform Landscaping, Phase 2 L1.43	10	01-Apr-25	14-Apr-25	12	Perform Landscaping, Phase 2 L1.43																							
SITEP2.1290	Install Sidewalks to Upper Soccer Fields, Phase 2 L1.43	10	01-Apr-25	14-Apr-25	12	Install Sidewalks to Upper Soccer Fields, Phase 2 L1.43																							
L1.43 COURTYARDS						25-Apr-25, L1.43 COURTYARDS																							
SITEP2.1310	Build Out Tennis Courts, Phase 2 L1.43	12	09-Apr-25	25-Apr-25	2	Build Out Tennis Courts, Phase 2 L1.43																							
L1.43 PAVING						21-Apr-25, L1.43 PAVING																							
SITEP2.1360	Install Subgrade at Parking Lots, Phase 2 L1.43	10	23-Sep-24*	04-Oct-24	103	Install Subgrade at Parking Lots, Phase 2 L1.43																							
SITEP2.1370	Install Curbing at Parking Lots, Phase 2 L1.43	10	07-Oct-24*	18-Oct-24	103	Install Curbing at Parking Lots, Phase 2 L1.43																							
SITEP2.1320	Install Binder at Parking Lots, Phase 2 L1.43	10	21-Oct-24*	01-Nov-24	103	Install Binder at Parking Lots, Phase 2 L1.43																							
SITEP2.1330	Install Topcourse Paving at Parking Lots, Phase 2 L1.43	10	01-Apr-25*	14-Apr-25	0	Install Topcourse Paving at Parking Lots, Phase 2 L1.43																							
SITEP2.1340	Linestripe, Markings and Install Site Signage, Phase 2 L1.43	4	15-Apr-25	21-Apr-25	8	Linestripe, Markings and Install Site Signage, Phase 2 L1.43																							
L1.44 SITEWORK FINISHES						01-May-25, L1.44 SITEWORK FINISHES																							
SITEP2.1380	Remove Temporary Parking Lot & Restore, Phase 2 L1.44	14	11-Apr-25	01-May-25	0	Remove Temporary Parking Lot & Restore, Phase 2 L1.44																							
PHASE 2 EXISTING HIGH SCHOOL ABATEMENT & DEMOLITION						16-Oct-24, PHASE 2 EXISTING HIGH SCHOOL ABATEMENT & DEMOLITION																							
DEMOP2.1080	Owner Move-out	12	05-Jun-24*	20-Jun-24	14	Owner Move-out																							
DEMOP2.1000	Cut, Cap & Make Safe, Existing High School, Existing High School	10	20-Jun-24*	03-Jul-24	14	Cut, Cap & Make Safe, Existing High School, Existing High School																							
DEMOP2.1010	Abatement & Selective Demolition, Existing High School	15	05-Jul-24	25-Jul-24	14	Abatement & Selective Demolition, Existing High School																							

First Person View PDF


Exported by masoncoudriet@ogind.com September 14, 2023 at 8:56:35 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County
Connecticut United States 06032


CAPTURE

DATE September 7, 2023 at 7:02:15 AM EDT
FLOOR L1.10 - OVERALL LAYOUT PLAN.pdf

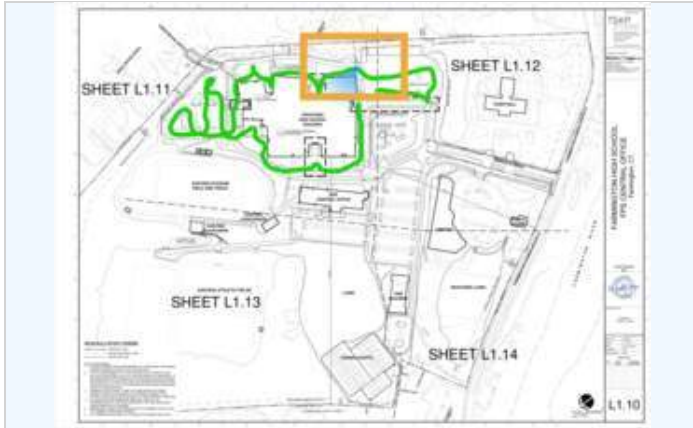

NOTES

Area A Exterior (East Side): Masonry Washed, Window Frames, & Glazing installation in progress.

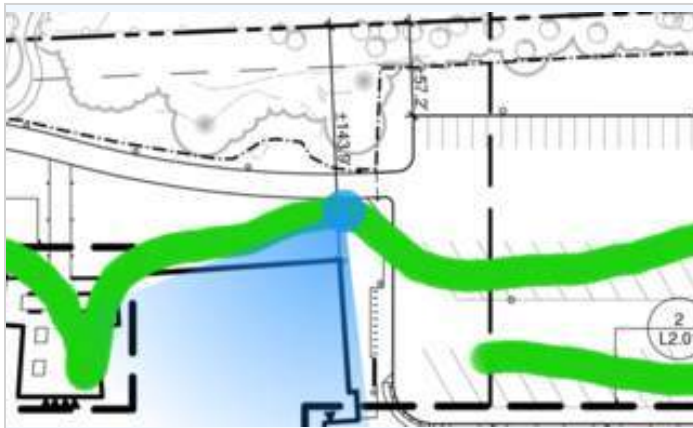

First Person View PDF


Exported by masoncoudriet@ogind.com September 14, 2023 at 8:18:58 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County Connecticut United States 06032

CAPTURE

DATE August 31, 2023 at 1:10:34 PM EDT
FLOOR A1.21 - SECOND FLOOR PLAN.pdf

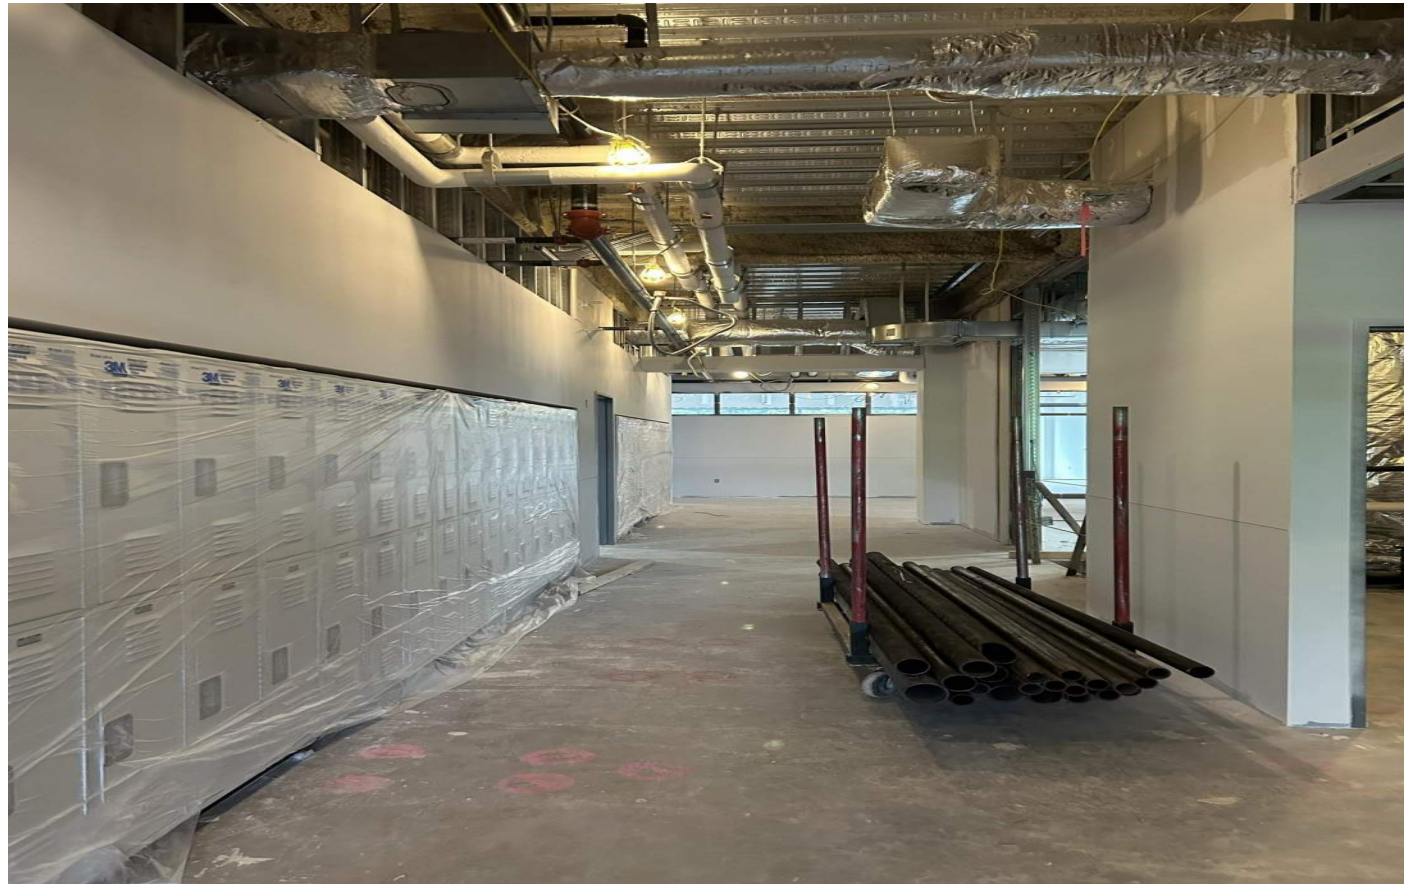

NOTES

Area A 2nd Floor Corridor: Metal Lockers installed and 1st coat of paint is done.

First Person View PDF


Exported by masoncoudriet@ogind.com September 14, 2023 at 8:57:16 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County
Connecticut United States 06032

CAPTURE

DATE August 29, 2023 at 1:26:11 PM EDT
FLOOR A1.31 - THIRD FLOOR PLAN.pdf

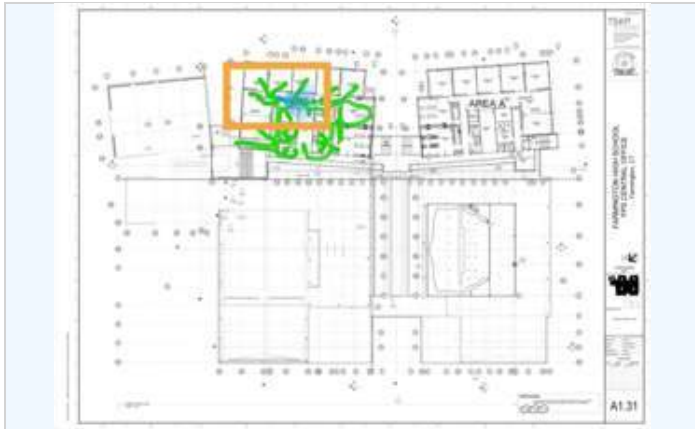

NOTES

Area B 3rd Floor: Drywall installed, taped, and sanded. Preparing for 1st coat paint.

First Person View PDF

Exported by masoncoudriet@ogind.com September 14, 2023 at 8:12:08 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County Connecticut United States 06032

CAPTURE

DATE September 11, 2023 at 8:44:16 AM EDT
FLOOR A1.21 - SECOND FLOOR PLAN.pdf



NOTES

Areas B/D 2nd Floor Concourse (South View): Rough Framing, Soffit Work, and Fire Protection Rough-In.



First Person View PDF

Exported by masoncoudriet@ogind.com September 14, 2023 at 8:19:48 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County Connecticut United States 06032

CAPTURE

DATE August 31, 2023 at 1:10:34 PM EDT
FLOOR A1.21 - SECOND FLOOR PLAN.pdf



NOTES

Area D Gymnasium: High view of Large Gym stepped seating. Area is ready for Mechanical and Electrical Rough-in

First Person View PDF


Exported by masoncoudriet@ogind.com September 14, 2023 at 8:14:18 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County Connecticut United States 06032

CAPTURE

DATE September 11, 2023 at 8:44:16 AM EDT
FLOOR A1.21 - SECOND FLOOR PLAN.pdf

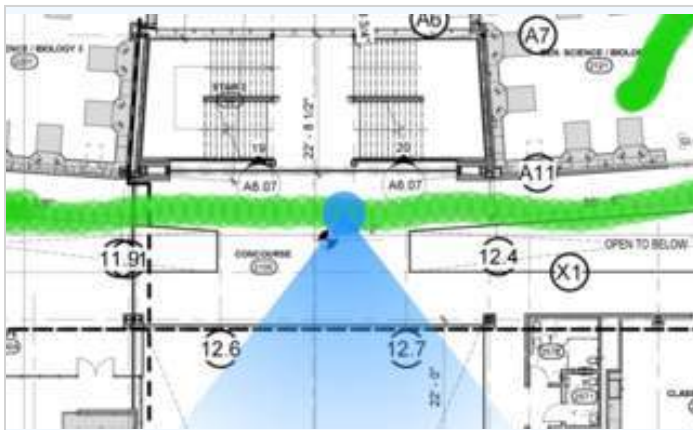

NOTES

Areas E Cafeteria: Concrete Slab on Grade Placement in progress with Steel Framing and Acoustical Decking complete on Sawtooth Skylights.

First Person View PDF

Exported by masoncoudriet@ogind.com September 14, 2023 at 8:21:05 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County
Connecticut United States 06032

CAPTURE

DATE August 31, 2023 at 1:10:34 PM EDT
FLOOR A1.21 - SECOND FLOOR PLAN.pdf



NOTES

Area E Auditorium: Concrete placement for lower seating area nearing completion. First step of Auditorium Seating Concrete Form Work in progress. Perimeter masonry walls started.

First Person View PDF



Exported by masoncoudriet@ogind.com September 14, 2023 at 8:16:50 AM EDT

PROJECT

NAME Farmington High School
CREATED December 1, 2022
LOCATION 10 Monteith Drive Farmington Hartford County Connecticut United States 06032

CAPTURE

DATE August 31, 2023 at 8:57:39 AM EDT
FLOOR L1.10 - OVERALL LAYOUT PLAN.pdf

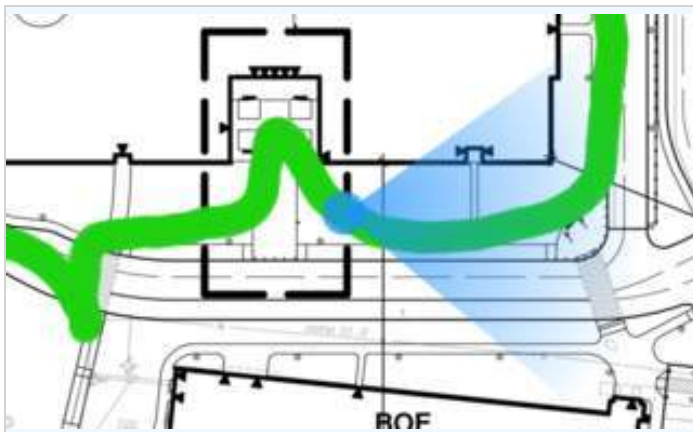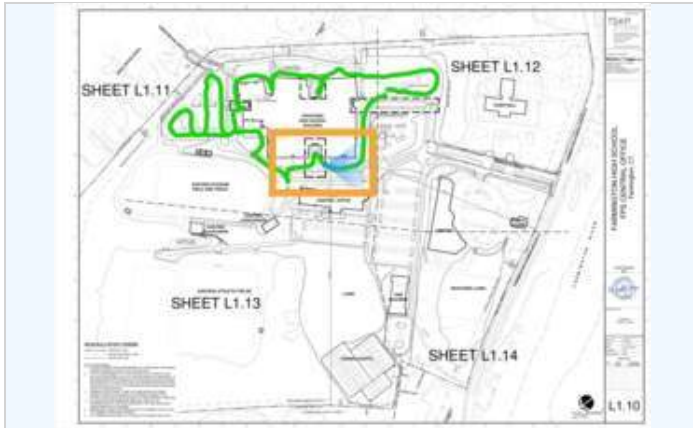

NOTES

Area E Exterior (West Side): Water Detention System #124 installation in progress.

Attachment B

FHS Building Project FE&E Technology



Categories

For Farmington High School, Areas A through E:

1. Category AVIT – Audio Visual Information Technology
2. Category COMP – Computer Equipment
3. Category AVEQAU – Audio Visual Equipment - Audio
4. Category AVFURN – Audio Visual Furniture
5. Category AVEQVI – Audio Visual Equipment - Video
6. Category AVINST – Audio Visual Instruments
7. Category LIEQ - Lighting Equipment

For Farmington Public Schools (Central Office), Area F:

8. Category AVIT – Audio Visual Information Technology



Existing Equipment (examples)

- Lampless projectors to other schools
- 2 Interactive Flat Panels to IAR
- A few large format LCD screens moved to IAR and WW (digital signage)
- Some AV equipment to IAR/WW
- Some AV equipment to new FHS (based on recent purchases in past 2 years)
- Desktop computers for staff (replaced in 2022-2023)
- 25 iMacs for Art Photo lab (purchased in 2022)



COMP - Computer Equipment

For Farmington High School, Areas A through E




AVEQAU - AV Equipment - Audio

For Farmington High School, Areas A through E



AVFURN - AV Furniture

For Farmington High School, Areas A through E

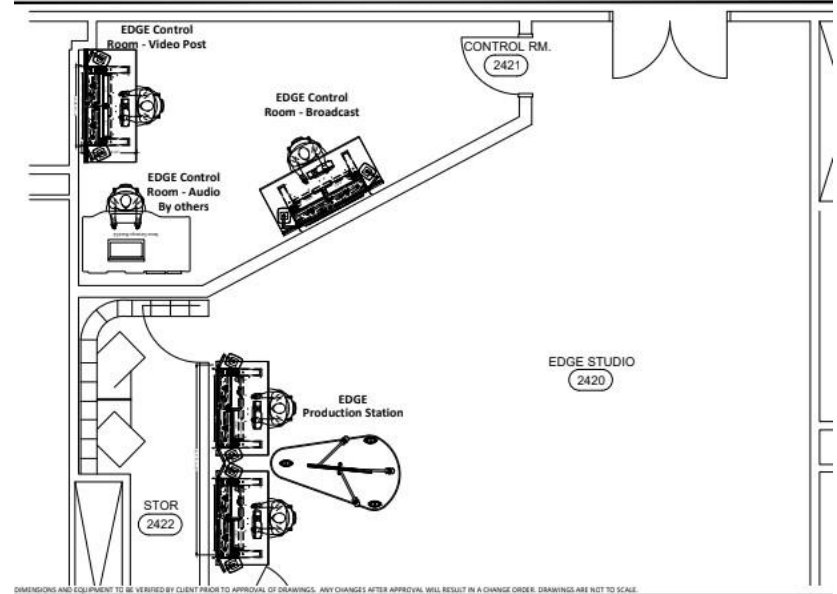

AVEQVI - AV Equipment - Video

For Farmington High School, Areas A through E



AVINST - AV Instruments

For Farmington High School, Areas A through E



LIEQ - Lighting Equipment

For Farmington High School, Areas A through E




*Actual Photo



AVIT - Audio Visual Info Tech

For Farmington Public Schools (Central Office), Area F



Cost Estimates - by Category

AVIT		\$667,370.00
COMP		\$90,249.00
AVEQAU		\$202,180.41
AVFURN		\$73,110.00
AVEQVI		\$203,917.86
AVINST		\$13,517.85
LIEQ		\$57,975.08
AVIT - CO		\$21,025.00
TOTAL ESTIMATE		\$1,329,345.20

